

## PK0-005 Dumps

### CompTIA Project+ Certification Exam

<https://www.certleader.com/PK0-005-dumps.html>



**NEW QUESTION 1**

**DRAG DROP -**

During a gate review meeting, the deliverable was rejected by the customer.

Review the dashboard.

Part 1: Drag and drop each task, placing them in the correct order based on the project change control process.

Part 2: Select the proper document(s) to be updated.

Part 1

Part 2

Change Control Process

1

?

2

?

3

?

4

?

5

Select the appropriate document(s) to update.

6

?

7

?

8

?

Dashboard

Drag and Drop

Perform a demonstration.

Define new requirements and record changes.

Update and test the deliverable.

Consult the RACI matrix.

Assess the schedule, risk, and cost.

Obtain a sign off.

Make an announcement on the company portal.

Part 1

Part 2

Change Control Process

1

?

2

?

3

?

4

?

5

Select the appropriate document(s) to update.

6

?

7

?

8

?

Dashboard

Question Options

Select the appropriate document(s) to update.

☐

Risk register

☐

Schedule

☐

Statement of work

☐

Organizational chart

☐

Change log

☐

Issues log

☐

WBS dictionary

- A. Mastered  
B. Not Mastered

**Answer:** A

**Explanation:**

The image displays two screenshots of a project management software interface, likely for a PMP exam simulation.

**Top Screenshot:**

- Part 1:** Change Control Process. A flowchart with 8 steps:
  - Define new requirements and record changes.
  - Assess the schedule, risk, and cost.
  - Update and test the deliverable.
  - Perform a demonstration.
  - Select the appropriate document(s) to update.
  - ?
  - ?
  - ?
- Part 2:** Drag and Drop. A list of 7 tasks:
  - Perform a demonstration.
  - Define new requirements and record changes.
  - Update and test the deliverable.
  - Consult the RACI matrix.
  - Assess the schedule, risk, and cost.
  - Obtain a sign off.
  - Make an announcement on the company portal.

**Bottom Screenshot:**

- Part 1:** Change Control Process. A flowchart with 8 steps, each with a dropdown menu:
  - ?
  - ?
  - ?
  - ?
  - Select the appropriate document(s) to update.
  - Statement of work
  - Schedule
  - Change log
- Part 2:** Question Options. A list of 7 items:
  - Risk register
  - Schedule
  - Statement of work
  - Organizational chart
  - Change log
  - Issues log
  - WBS dictionary

#### NEW QUESTION 2

During a quality analysis review, the causes of several issues have been highlighted. Which of the following should the project manager use to identify the MOST important causes?

- A. Ishikawa diagram
- B. Scatter diagram
- C. Pareto chart
- D. Decision tree

**Answer: C**

#### NEW QUESTION 3

A project team gathers weekly to review its progress. Which of the following is the project manager MOST likely to have prepared to ensure team members who are absent remain informed about assignments?

- A. Status report
- B. Project plan
- C. Change log
- D. Meeting minutes

**Answer: D**

#### NEW QUESTION 4

During the stabilization phase for recently deployed software, an end user reports a bug that is compromising data integrity. Which of the following tools will the project manager MOST likely use?

- A. Issue log
- B. Defect log
- C. Change log
- D. Task board

**Answer: B**

#### NEW QUESTION 5

The project team determines that software installation can only begin after the desktops have been installed and can be powered on. Which of the following dependencies does this represent?

- A. External
- B. Internal
- C. Mandatory
- D. Discretionary

**Answer:** B

#### NEW QUESTION 6


Due to budgetary and time constraints, a PM scheduled a meeting with all stakeholders during the planning phase to review the requirements and come to an agreement on the minimum viable product that would be acceptable. Which of the following would be used to document this input?

- A. Project change management plan
- B. Project management plan Most Voted
- C. Project transition plan
- D. Project communication plan

**Answer:** B

#### NEW QUESTION 7

A project team was instructed to refurbish old desktops. The following provides the details of the issues observed:

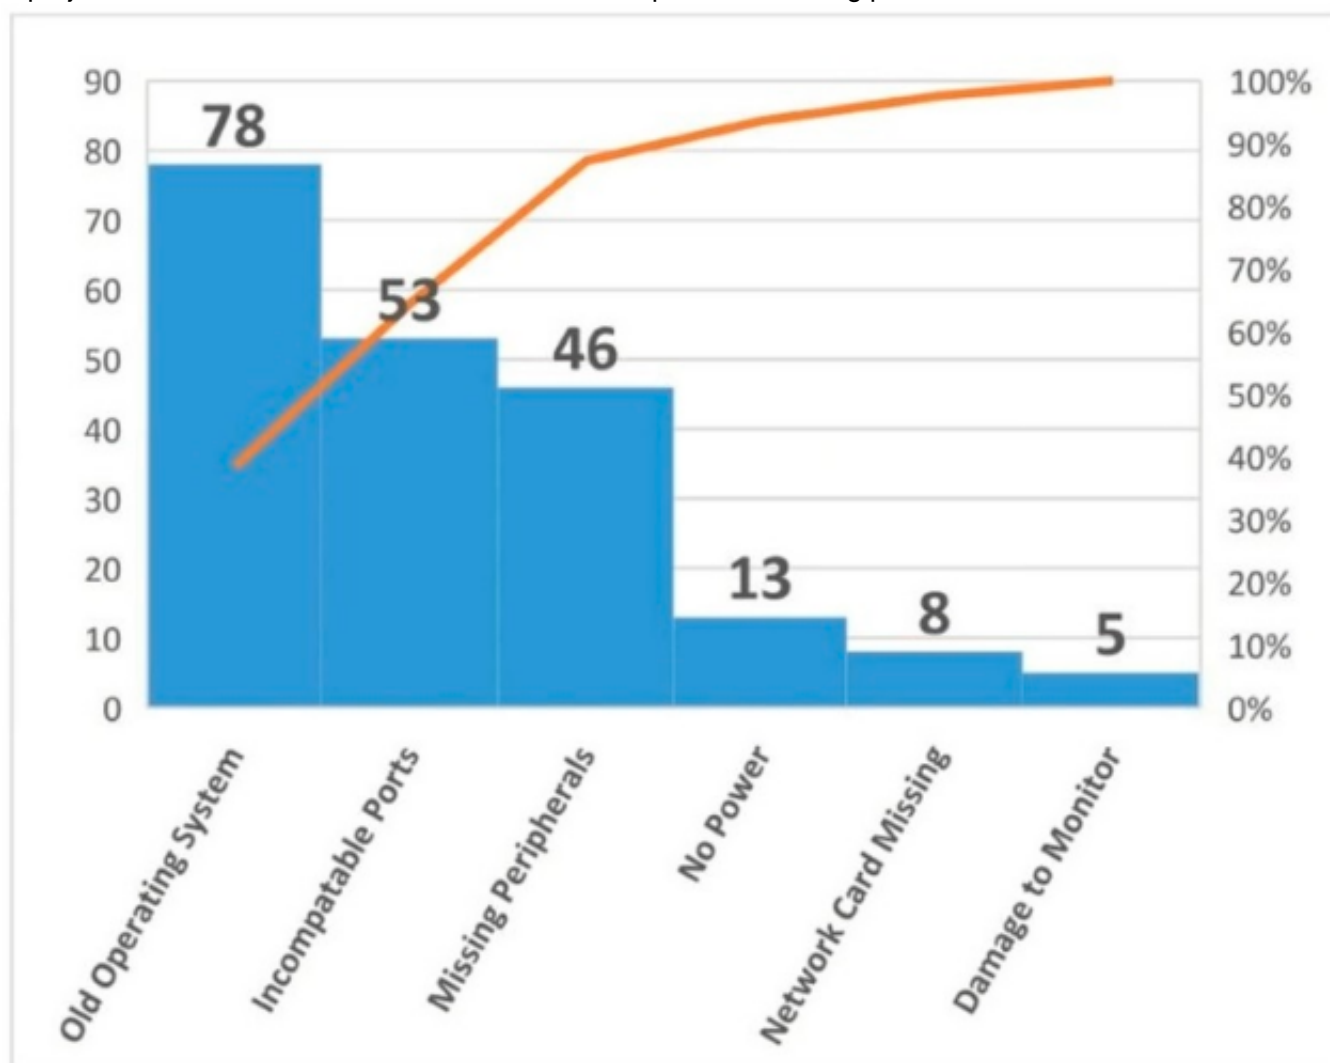

- A. Replace missing peripherals because this process can be easy and less costly.
- B. An old operating system issue has the most amount of occurrences.
- C. Damage to the monitor has the highest percentage.
- D. Address each issue as discovered to avoid rework.

**Answer:** A

#### NEW QUESTION 8

A project manager was not part of a contract negotiation. The project manager is concerned that stakeholders will expect the project to achieve deliverables requested in the RFP. Which of the following documents should the project manager produce FIRST to start communication about the boundaries of the project?

- A. Milestone chart
- B. Work breakdown structure
- C. Project charter
- D. Detailed scope statement

**Answer:** C

#### NEW QUESTION 9

In a functional organization, a project has been completed successfully. Which of the following actions would the project manager MOST likely perform?

- A. Assemble a new project with existing resources.
- B. Obtain the final report from release management.
- C. Notify the functional manager that resources are released.
- D. Allocate resources in a different project.

**Answer:** B

**NEW QUESTION 10**

A stakeholder works in a remote location and has not been replying to emails. The Internet service in that location is intermittent, and the stakeholder prefers to be contacted by telephone. Which of the following artifacts should the project manager have prepared to avoid this situation?

- A. Responsibility assignment matrix
- B. Acceptable communication channels
- C. Risk registry
- D. Staff directory

**Answer:** B

**NEW QUESTION 10**

Due to multiple changes, the sign-off for the project scope baseline is delayed. The project sponsor has restricted the budget for this project. Which of the following should the project manager MOST likely do to move forward?

- A. Communicate with the affected stakeholders.
- B. Initiate a formal change request to modify the cost.
- C. Adjust the scope to stay within the cost.
- D. Set a new cost using a lightweight estimation method.

**Answer:** C

**NEW QUESTION 14**

An opportunity emerged in the middle of a project life cycle. Which of the following is the BEST action for the project manager to take?

- A. Exploit the risk.
- B. Accept the risk.
- C. Avoid the risk.
- D. Transfer the risk.

**Answer:** D

**NEW QUESTION 18**

A project manager was just assigned to a new project. Which of the following activities should the project manager undertake after accepting the project? (Choose two.)

- A. Review the detailed plan.
- B. Develop a preliminary scope.
- C. Develop a transition plan.
- D. Develop a project management plan.
- E. Review the resource pool.
- F. Review the project objectives.

**Answer:** AF

**NEW QUESTION 20**

A program manager is reviewing the project portfolio and prioritizing each project based on the company's strategic plan. Which of the following should be considered in this evaluation? (Choose two.)

- A. Company vision
- B. Global environment
- C. Brand value
- D. Mission statement
- E. Portfolio budget
- F. Local legislation

**Answer:** AB

**NEW QUESTION 23**

A visual that displays team progress was created for stand-up meetings. Which of the following BEST describes what is being represented on the visual?

- A. Decision board
- B. Whiteboard
- C. Task board
- D. Dashboard

**Answer:** D

**NEW QUESTION 24**

A project manager is assigned to a multinational project with team members from different continents. Which of the following is the MOST important aspect for the project manager to consider?

- A. Resource allocation

- B. Communication security
- C. Technological factors
- D. Cultural differences

**Answer:** D

**NEW QUESTION 27**

.....

## Thank You for Trying Our Product

\* 100% Pass or Money Back

All our products come with a 90-day Money Back Guarantee.

\* One year free update

You can enjoy free update one year. 24x7 online support.

\* Trusted by Millions

We currently serve more than 30,000,000 customers.

\* Shop Securely

All transactions are protected by VeriSign!

**100% Pass Your PK0-005 Exam with Our Prep Materials Via below:**

<https://www.certleader.com/PK0-005-dumps.html>
