

Exam Questions PK0-005

CompTIA Project+ Certification Exam

<https://www.2passeasy.com/dumps/PK0-005/>



NEW QUESTION 1

Which of the following is an activity that should be used in the closing phase of a project to support the project triple constraint?

- A. Evaluating the project
- B. Releasing the resources
- C. Closing the contracts
- D. Reconciling the budget

Answer: A

NEW QUESTION 2

As part of the planning phase, a PM has defined tasks, durations, resources, and costs. Which of the following is the NEXT step in the process?

- A. Update the work breakdown structure.
- B. Review the backlog.
- C. Seek baseline approval.
- D. Establish the resource pool.

Answer: C

NEW QUESTION 3

A project manager realizes that a project will not be completed on time due to resource constraints. Which of the following actions should the project manager take NEXT?

- A. Trigger the contingency plan and communicate with the stakeholders.
- B. Work with the functional managers to create a work-around.
- C. Submit a change request to the change control board.
- D. Transfer the risk by hiring a new vendor who was successful on a previous project.
- E. Set up an escalation meeting with the sponsor.

Answer: A

NEW QUESTION 4

During a staff meeting, a project manager voices a concern about the client billing rate for a particular engineer. Which of the following documents would the project manager need in order to find this information?

- A. SLA
- B. TOR
- C. SOW
- D. NDA

Answer: AB

NEW QUESTION 5

Which of the following should occur when implementing an IT infrastructure change that takes risks into consideration?

- A. Approving the change request
- B. Developing a rollback plan
- C. Gathering necessary resources
- D. Defining requirements

Answer: B

NEW QUESTION 6

A project manager is in the closing phase of an IT asset refresh project that involves the disposal of several computers. The project sponsor notified the project manager that the company recently received a penalty as a result of disposing of some computers improperly. Which of the following should have been considered during initial planning to prevent this situation?

- A. ESG
- B. PHI
- C. PII
- D. ROIL

Answer: A

NEW QUESTION 7

The project team determines that software installation can only begin after the desktops have been installed and can be powered on. Which of the following dependencies does this represent?

- A. External
- B. Internal
- C. Mandatory
- D. Discretionary

Answer:

B

NEW QUESTION 8

A hurricane delays the shipment of critical equipment for a project. Which of the following is BEST to use to document the effects of this delay?

- A. Issue log
- B. Gantt chart
- C. Milestone chart
- D. Change control log

Answer: C

NEW QUESTION 9

A project manager was not part of a contract negotiation. The project manager is concerned that stakeholders will expect the project to achieve deliverables requested in the RFP. Which of the following documents should the project manager produce FIRST to start communication about the boundaries of the project?

- A. Milestone chart
- B. Work breakdown structure
- C. Project charter
- D. Detailed scope statement

Answer: C

NEW QUESTION 10

While developing a project charter, a PM discovers that some of the legal requirements have not been addressed during the project concept preparation, which could result in significant financial penalties against the organization. The PM knows that implementation of appropriate changes is costly and will exceed the budget and scope of the project. Which of the following should the PM do FIRST?

- A. Escalate the finding to the change control board.
- B. Add a risk to the risk register for validation.
- C. Consult the RACI matrix to identify ownership of the risk.
- D. Have a meeting with the project sponsor and main stakeholders.

Answer: D

NEW QUESTION 10

A stakeholder works in a remote location and has not been replying to emails. The Internet service in that location is intermittent, and the stakeholder prefers to be contacted by telephone. Which of the following artifacts should the project manager have prepared to avoid this situation?

- A. Responsibility assignment matrix
- B. Acceptable communication channels
- C. Risk registry
- D. Staff directory

Answer: B

NEW QUESTION 15

After a release, the project sponsor received an escalation from an executive about the extension of the downtime after the scheduled window. Which of the following should be added to the issue log?

- A. Continuous integration
- B. Rollback plan
- C. Customer notification
- D. Automated testing

Answer: B

NEW QUESTION 19

Due to multiple changes, the sign-off for the project scope baseline is delayed. The project sponsor has restricted the budget for this project. Which of the following should the project manager MOST likely do to move forward?

- A. Communicate with the affected stakeholders.
- B. Initiate a formal change request to modify the cost.
- C. Adjust the scope to stay within the cost.
- D. Set a new cost using a lightweight estimation method.

Answer: C


NEW QUESTION 23

As a result of an approved change, the project manager updates the project plan with the newest project end date. Which of the following change control processes should the project manager complete NEXT?

- A. Document the request in the change control log.
- B. Communicate the change deployment.
- C. Conduct an impact assessment.
- D. Implement the change.

Answer: C

Explanation:

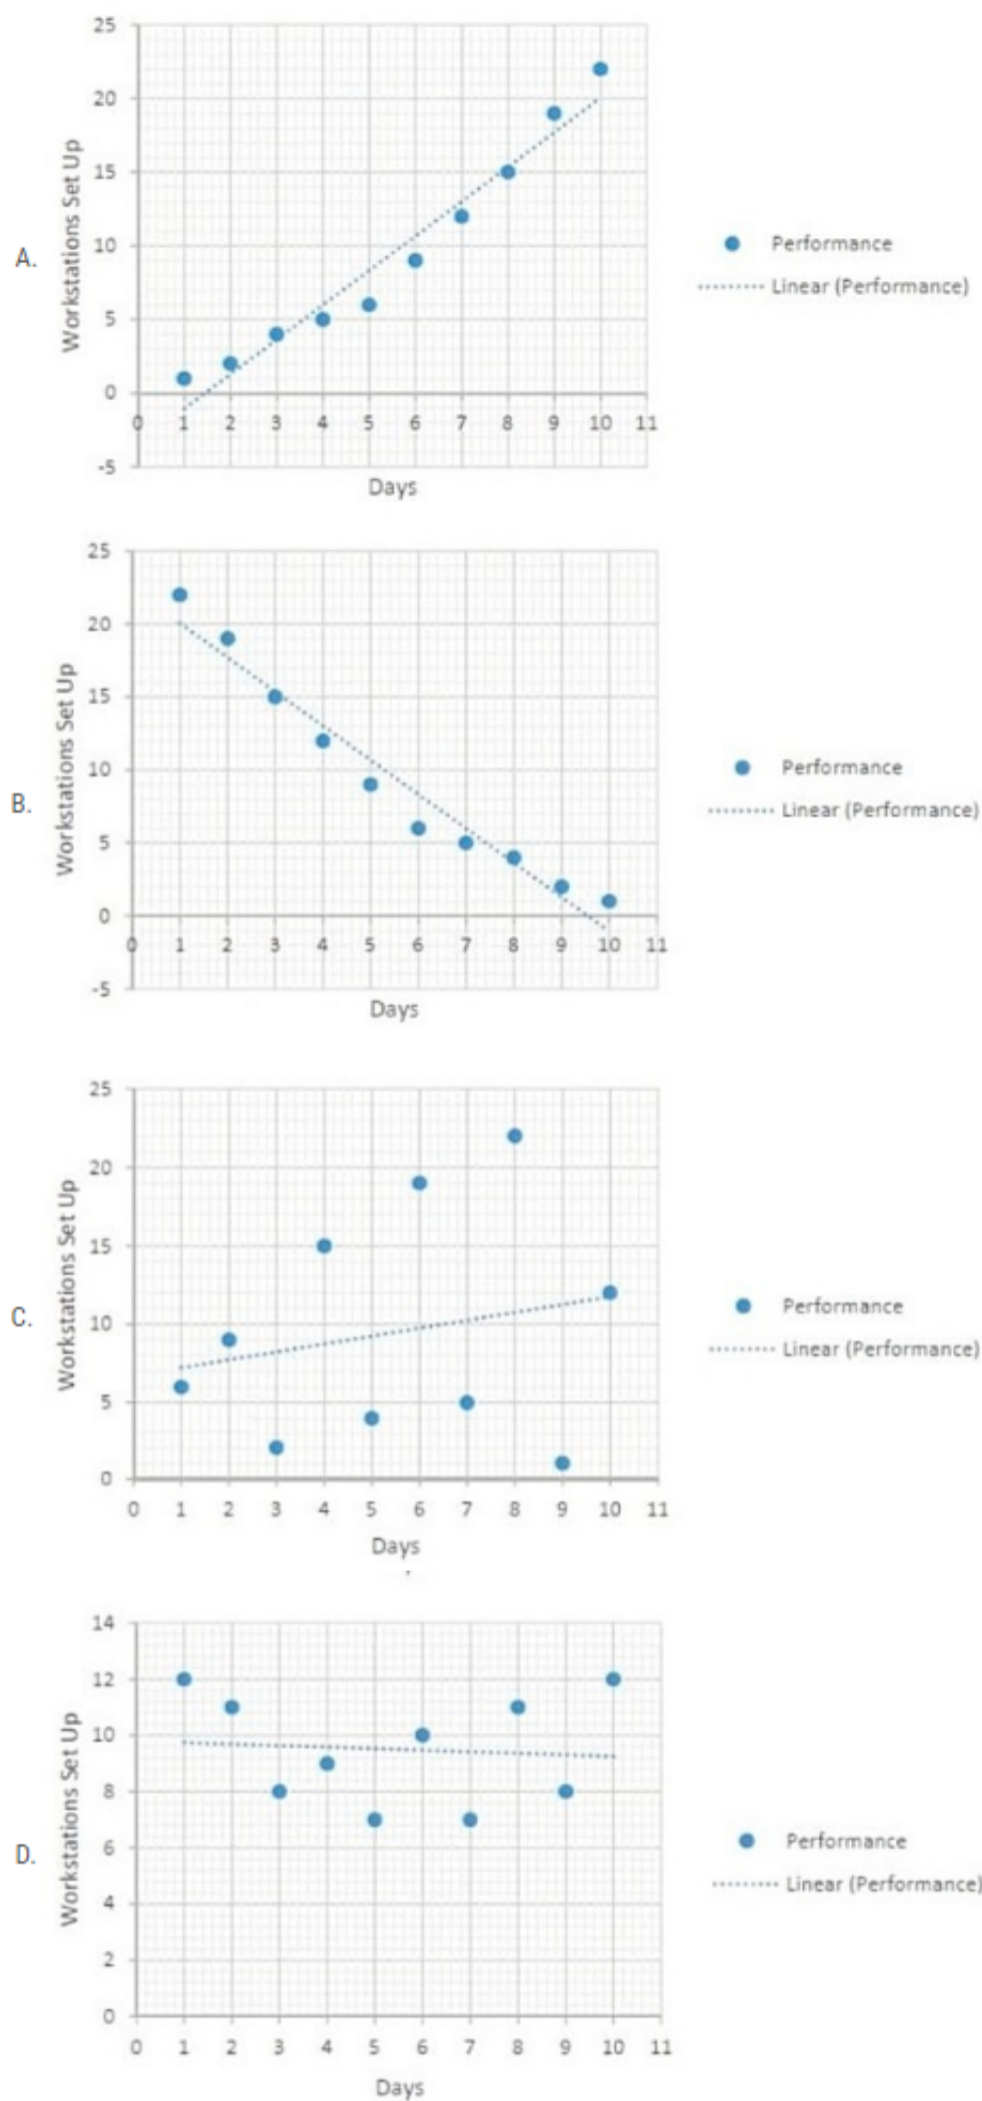

NEW QUESTION 28

A program manager is reviewing the project portfolio and prioritizing each project based on the company's strategic plan. Which of the following should be considered in this evaluation? (Choose two.)

- A. Company vision
- B. Global environment
- C. Brand value
- D. Mission statement
- E. Portfolio budget
- F. Local legislation

Answer: AB

NEW QUESTION 29

Halfway through a project, the sponsor states that the project is taking too long to complete. Which of the following should the project manager consult?

- A. Gantt chart
- B. Maintenance window schedule
- C. Functional requirements
- D. Test results

Answer: A

NEW QUESTION 30

A project manager is assigned to a multinational project with team members from different continents. Which of the following is the MOST important aspect for the project manager to consider?

- A. Resource allocation
- B. Communication security
- C. Technological factors
- D. Cultural differences

Answer: D

NEW QUESTION 32

A critical business initiative introduced new processes and technology to the organization. Which of the following approaches should be used to ensure the deliverables are increasingly adopted and leveraged by the organization over time?

- A. Creation of a social news forum
- B. Management directives to use the new system
- C. New user kickoff meeting
- D. Monthly feedback and training sessions

Answer: D

NEW QUESTION 33

.....

THANKS FOR TRYING THE DEMO OF OUR PRODUCT

Visit Our Site to Purchase the Full Set of Actual PK0-005 Exam Questions With Answers.

We Also Provide Practice Exam Software That Simulates Real Exam Environment And Has Many Self-Assessment Features. Order the PK0-005 Product From:

<https://www.2passeasy.com/dumps/PK0-005/>

Money Back Guarantee

PK0-005 Practice Exam Features:

- * PK0-005 Questions and Answers Updated Frequently
- * PK0-005 Practice Questions Verified by Expert Senior Certified Staff
- * PK0-005 Most Realistic Questions that Guarantee you a Pass on Your FirstTry
- * PK0-005 Practice Test Questions in Multiple Choice Formats and Updatesfor 1 Year
