

Exam Questions PK0-005

CompTIA Project+ Certification Exam

<https://www.2passeasy.com/dumps/PK0-005/>



NEW QUESTION 1

Due to multiple changes, the sign-off for the project scope baseline is delayed. The project sponsor has restricted the budget for this project. Which of the following should the project manager MOST likely do to move forward?

- A. Communicate with the affected stakeholders.
- B. Initiate a formal change request to modify the cost
- C. Adjust the scope to stay within the cost.
- D. Set a new cost using a lightweight estimation method.


Answer: A

Explanation:

The project manager should communicate with the affected stakeholders first after realizing that the sign-off for the project scope baseline is delayed due to multiple changes and that the budget for this project is restricted by the project sponsor. The affected stakeholders are those who have an interest or influence on the project and may be impacted by any changes or delays. Communicating with them can help to explain the situation, assess the impact, seek feedback, and manage expectations.

NEW QUESTION 2

Given the following network diagram:

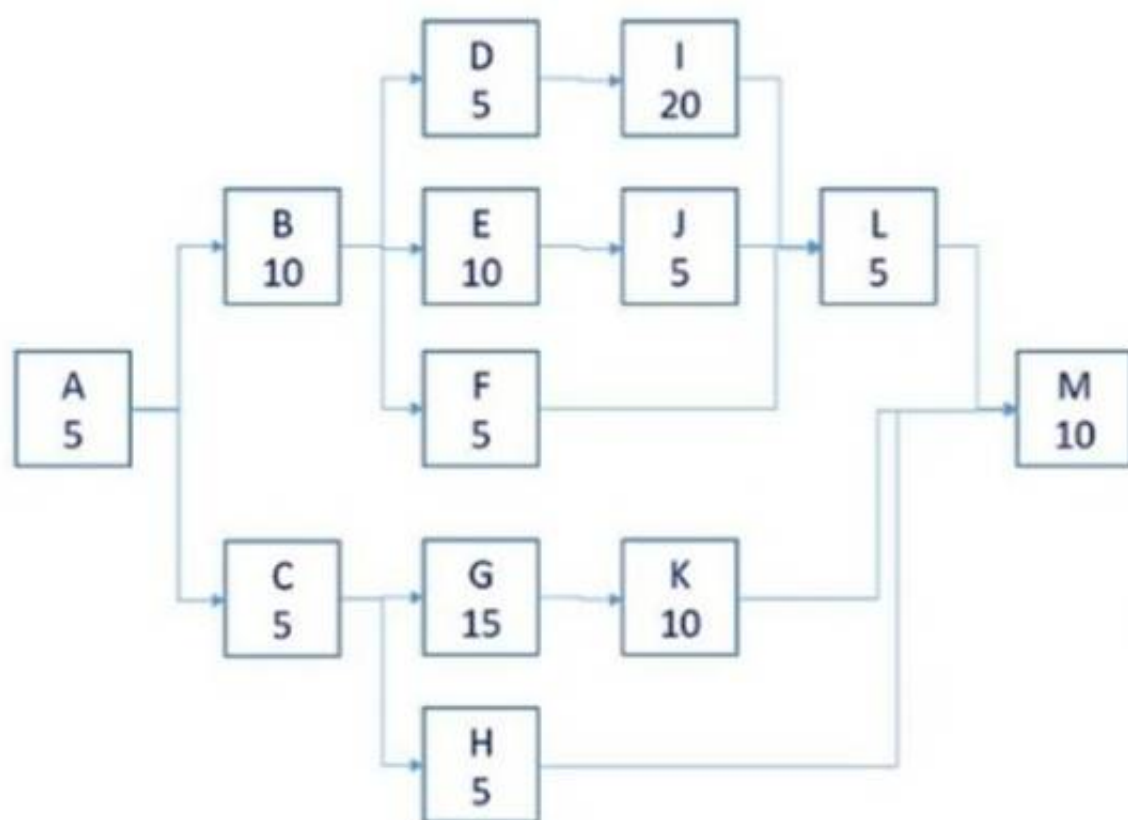

Which of the following is the critical path?

- A. A-C-G-K-M
- B. A-B-D-I-L-M
- C. A-B-E-J-L-M
- D. A-B-F-L-M

Answer: A

Explanation:

The critical path is the sequence of tasks that determines the minimum project duration. It is the longest path through the network diagram and has the least amount of slack or float. Based on the provided network diagram, the critical path is A-C-G-K-M, which has the longest total duration when adding up the individual task durations. References = The concept of the critical path is covered in the CompTIA Project+ Certification Study Guide¹. For more detailed information on how to calculate and identify the critical path in project management, you can refer to the study guide and other project management resources².

NEW QUESTION 3

Which of the following aspects are true of agile as compared to waterfall? (Select two).

- A. Agile works through larger integrated teams.
- B. Agile promotes project manager ownership over deliverables.
- C. Agile reinforces the importance of comprehensive documentation.
- D. Agile has more customer involvement throughout development.
- E. Agile is more flexible to allow for changes in scope.
- F. Agile is comprised of well-defined phases.

Answer: DE

Explanation:

Agile is a project management methodology that emphasizes customer collaboration, feedback, and adaptation throughout the project life cycle. Agile teams work in short iterations, called sprints, and deliver working increments of the product or service to the customer for review and approval. Agile teams can also respond to changing requirements and priorities by adjusting the scope, schedule, or quality of the project¹². Waterfall, on the other hand, is a project management methodology that follows a linear and sequential process, where each phase of the project must be completed before moving on to the next one. Waterfall teams work with a fixed scope, schedule, and quality, and deliver the final product or service to the customer at the end of the project. Waterfall teams have less

customer involvement and flexibility during the project development³⁴.

NEW QUESTION 4

Which of the following are primary features provided by a standard IaaS solution? (Select two).

- A. Encryption
- B. Storage
- C. Networking
- D. User interface
- E. Access
- F. Database

Answer: BC

Explanation:

According to What is Logging as a Service (LaaS)? - LogicMonitor, LaaS is a cloud-based log management platform that simplifies the management of infrastructure and application logs. LaaS offers a central location where you can store, analyze and visualize the content of all your logs. It works by ingesting logs from different sources, such as web servers, IoT devices, database servers and more. It then provides actionable output by organizing and restructuring the information within these logs. Therefore, storage and networking are primary features provided by a standard LaaS solution, as they enable the collection and transmission of logs from various sources to a centralized platform. Encryption, user interface, access, and database are not primary features of LaaS, as they are either optional or secondary aspects of the service.

NEW QUESTION 5

Which of the following activities would a project manager perform during the closing phase? (Select THREE).

- A. Lessons learned
- B. Risk analysis
- C. Removing resources
- D. Acquiring resources
- E. Statement of work sign-off
- F. Stakeholder analysis
- G. Removing access

Answer: ACG

Explanation:

Lessons learned, removing resources, and removing access are activities that a project manager would perform during the closing phase of a project. Lessons learned is a process of collecting and documenting the knowledge and experience gained from a project for future reference and improvement. Removing resources is a process of releasing or reallocating any human or material resources that were used for the project. Removing access is a process of revoking any permissions or privileges that were granted to the project team members or stakeholders for accessing any systems or data related to the project. These activities can help to finalize and close a project successfully and ensure that all deliverables are transferred, all documentation is approved and archived, all contracts are closed, and all stakeholders are satisfied.

NEW QUESTION 6

A project manager was just assigned to a new project. Which of the following activities should the project manager undertake after accepting the project? (Select TWO).

- A. Review the detailed plan.
- B. Develop a preliminary scope.
- C. Develop a transition plan.
- D. Develop a project management plan.
- E. Review the resource pool.
- F. Review the project objectives.

Answer: EF

Explanation:

Review the resource pool and review the project objectives are activities that the project manager should undertake after accepting a new project. Reviewing the resource pool involves identifying and evaluating the availability, skills, and competencies of the human and material resources that are needed for the project. Reviewing the project objectives involves understanding and clarifying the expected outcomes and benefits of the project and how they align with the organizational strategy and stakeholder expectations. These activities can help to plan and execute the project effectively and efficiently.

NEW QUESTION 7

Which of the following activities would be performed during the project closure phase when the waterfall methodology is being used? (Select two).

- A. Creating a backlog
- B. Managing the quality of deliverables
- C. Updating the issue log
- D. Performing a risk assessment
- E. Validating the deliverables
- F. Reconciling the project budget

Answer: EF

Explanation:

During the project closure phase in the waterfall methodology, it is crucial to validate the deliverables to ensure that all project requirements have been met and the project outputs are complete and satisfactory. Additionally, reconciling the project budget is performed to ensure all financial records are accurate and reflect the actual project costs, which is essential for the formal closing of the project.

References = CompTIA Project+ Certification Study Guide (PK0-005)

NEW QUESTION 8

A team is analyzing the backlog in order to decide what to include in the next sprint. Which of the following aspects is the most important for the team to take into consideration?

- A. Time to be fixed
- B. Impact to project
- C. Issue category
- D. Resource availability

Answer: B

Explanation:

When analyzing the backlog to decide what to include in the next sprint, the most important aspect to consider is the impact to the project. This involves assessing which items will provide the most value and contribute significantly towards achieving the project goals. It's crucial to prioritize work that has the highest impact on the project's success.

References = The answer is based on standard agile project management practices, particularly in the context of sprint planning where prioritization is key. For detailed information, please refer to the CompTIA Project+ Study Guide and other official CompTIA resources

NEW QUESTION 9

Which of the following tools is best to use for storing lessons learned?

- A. Whiteboard
- B. Wiki knowledge base
- C. Content management system
- D. Workflow platform

Answer: B

Explanation:

A wiki knowledge base is a collaborative online platform that allows users to create, edit, and share information about a specific topic or domain¹. A wiki knowledge base is best to use for storing lessons learned because it enables easy access, retrieval, and update of the lessons learned by project teams and stakeholders². A wiki knowledge base can also support keyword search, version control, and linking of related documents³. A wiki knowledge base is different from a whiteboard, which is a physical or digital board that can be used for brainstorming, sketching, or presenting ideas; a content management system, which is a software application that allows users to create, manage, and publish digital content; and a workflow platform, which is a software tool that automates and streamlines business processes⁴. References = CompTIA Project+ Study Guide: Exam PK0-005, 3rd Edition, Chapter 14: Closing the Project, page 403; Capturing Lessons Learned in Project Management [2023] • Asana, Different types of lessons learned sessions and Lessons Learned Process in Project Management sections; Project Management Lessons Learned | Smartsheet, What Are Lessons Learned in Project Management? and Lessons Learned Process in Project Management sections; How to Do Lessons Learned in Project Management, Store and Retrieve sections.

NEW QUESTION 10

A developer focused on a single story during an entire sprint. The story was underestimated and, therefore, was not completed. Which of the following steps should the Scrum team take next?

- A. Assign more resources to complete similar stories in the future.
- B. Break the stories into workable items that can be completed within one sprint.
- C. Extend the sprint duration when required with the approval of the product owner.
- D. Release the current progress into production and carry over the rest of the code for the next sprint.

Answer: B

Explanation:

The Scrum team should break the stories into workable items that can be completed within one sprint, which is a time-boxed period of 7 to 30 days, during which the team delivers a potentially releasable product increment. Breaking the stories into smaller and more manageable items can help the team to estimate them more accurately, plan them more effectively, and deliver them more reliably. Breaking the stories also aligns with the agile principle of delivering working software frequently and satisfying the customer through early and continuous delivery of valuable software.

The other options are not the best steps for the Scrum team to take next. Assigning more resources to complete similar stories in the future may not solve the problem of underestimation, and may introduce additional complexity and communication overhead. Extending the sprint duration when required with the approval of the product owner may compromise the consistency and predictability of the Scrum process, and may delay the feedback and validation from the stakeholders. Releasing the current progress into production and carrying over the rest of the code for the next sprint may result in an incomplete or unstable product increment, and may violate the definition of done, which is a shared understanding of the quality criteria that the product increment must meet. References = CompTIA Project+ Study Guide: Exam PK0-005, 3rd Edition, Chapter 5: Project Scope Management¹; CompTIA Project+ Certification Study Guide, 3rd Edition, Chapter 5: Project Scope Management²; The 3 Scrum Roles and Responsibilities Explained³; Implementation of Scrum - 7 Steps for an Effective Process⁴

NEW QUESTION 10

A visual that displays team progress was created for stand-up meetings. Which of the following BEST describes what is being represented on the visual?

- A. Decision board
- B. Whiteboard
- C. Task board
- D. Dashboard

Answer: C

Explanation:

A task board is a visual tool that displays team progress for stand-up meetings. A task board usually consists of columns that represent different stages or statuses of tasks, such as to do, in progress, done, or blocked. Each task is represented by a card or sticky note that can be moved across the columns as the task progresses. A task board can help to facilitate communication, collaboration, and transparency among team members and stakeholders. It can also help to track and manage work flow, prioritize tasks, identify bottlenecks, and resolve issues³

NEW QUESTION 13

During a status meeting, the development team reviews work and finds an unforeseen dependency on one of the critical project activities. As a result, the project will most likely be delayed. Which of the following actions should the project manager MOST likely perform?

- A. Work with the project scheduler to update the project timeline.
- B. Communicate to the stakeholders about the updated timeline.
- C. Ask the development team to fast-track upcoming activities.
- D. Add two resources so the critical activities will finish on time.

Answer: A

Explanation:

Work with the project scheduler to update the project timeline. The project manager should work with the project scheduler to update the project timeline after finding an unforeseen dependency on one of the critical project activities that will most likely cause a delay. The project scheduler is a person or a tool that helps plan, schedule, monitor, and control the project activities and resources. The project scheduler can help the project manager to assess the impact of the dependency on the project schedule and identify any possible ways to mitigate or resolve it. The project scheduler can also help to update the project timeline with the revised dates and durations of the project activities and communicate them to the relevant stakeholders.

NEW QUESTION 15

A program manager is reviewing the project portfolio and prioritizing each project based on the company's strategic plan. Which of the following should be considered in this evaluation? (Select TWO).

- A. Company vision
- B. Global environment
- C. Brand value
- D. Mission statement
- E. Portfolio budget
- F. Local legislation

Answer: AD

Explanation:

Company vision and mission statement should be considered in the evaluation of the project portfolio based on the company's strategic plan. Company vision is a statement that describes the long-term aspirations and desired future state of the organization. Company mission statement is a statement that defines the core purpose and values of the organization and how it serves its customers and stakeholders. These statements provide direction and guidance for the strategic planning and decision making of the organization. They also help to align the project portfolio with the organizational goals and objectives and ensure that the projects and programs in the portfolio deliver value and benefits to the organization¹²

NEW QUESTION 16

Before a configuration can be made to a system in development, a document containing information about how the new system will interact with other systems within the organization needs to be written. Which of the following relationships best describes this scenario?

- A. Start-to-start
- B. Start-to-finish
- C. Finish-to-finish
- D. Finish-to-start

Answer: D

Explanation:

A finish-to-start relationship is a type of logical dependency between two tasks, in which the first task must be completed before the second task can start. In this scenario, the document containing information about how the new system will interact with other systems within the organization is a prerequisite for the configuration of the system in development. Therefore, the document writing task must finish before the configuration task can start, which is a finish-to-start relationship. References = CompTIA Project+ Study Guide: Exam PK0-005, 3rd Edition, Chapter 6: Schedule Management¹; CompTIA Project+ Certification Study Guide, 3rd Edition, Chapter 6: Schedule Management²

NEW QUESTION 20

During the testing phase of a project, the legal department rejected a deliverable due to compliance issues. The project manager reviewed the risk register and triggered the mitigation plan for this item. Which of the following documents should the project manager update next?

- A. Schedule
- B. Status report
- C. Issue log
- D. Task board

Answer: C

Explanation:

An issue log is a document that records and tracks any issues that arise during a project and how they are resolved¹. It is different from a risk register, which records and tracks potential risks that may or may not occur during a project². When a risk becomes an issue, it means that it has occurred and has a negative impact on the project. Therefore, the project manager should update the issue log next to document the compliance issue, its cause, its impact, its priority, its owner, and its resolution status³. Updating the issue log will help the project manager communicate the issue to the stakeholders, monitor the progress of the mitigation plan, and prevent similar issues from happening again⁴. References = CompTIA Project+ PK0-005 Certification Study Guide, Chapter 11: Executing Projects Part 2, page 331; Project Risk Mitigation Guide + Starter Kit | Smartsheet, Risk Register section; How to Make a Risk Management Plan (Template Included) - ProjectManager, Risk Register section; Issue Log - Project Management Knowledge, Introduction section; Issue Log Template: Free Download | ProjectManager, Introduction and How to Use an Issue Log sections.

NEW QUESTION 23

A project manager is in the closing phase of an IT asset refresh project that involves the disposal of several computers. The project sponsor notified the project manager that the company recently received a penalty as a result of disposing of some computers improperly. Which of the following should have been considered during initial planning to prevent this situation?

- A. ESG
- B. PHI
- C. PII
- D. ROI

Answer: A

Explanation:

The project manager should have considered environmental, social, and governance (ESG) factors during initial planning to prevent the situation of receiving a penalty for disposing of some computers improperly. ESG factors are criteria that measure the sustainability and ethical impact of an organization's activities. They include aspects such as environmental protection, social responsibility, human rights, diversity, and corporate governance. Considering ESG factors can help to reduce risks, improve reputation, and enhance performance of an organization¹²

NEW QUESTION 25

Which of the following is an activity that should be used in the closing phase of a project to support the project triple constraint?

- A. Evaluating the project
- B. Releasing the resources
- C. Closing the contracts
- D. Reconciling the budget

Answer: A

Explanation:

Evaluating the project is an activity that should be used in the closing phase of a project to support the project triple constraint. This involves reviewing the project plan, deliverables, and outcomes to ensure they meet the project objectives and requirements. References: CompTIA Project+ Study Guide Section 4.4.4

NEW QUESTION 26

After months of recruiting, a team finally found the right candidate for a very specific coding language assignment. Due to this delay, the team has a tight timeline without any float. A day before the candidate is scheduled to join the team, the project manager realizes the candidate has a non-compete agreement from the previous employer. Which of the following should the project manager do?

- A. Withdraw the offer to the candidate and raise this as a risk.
- B. Ignore a potential lawsuit since this is a critical project.
- C. Use a third-party company for the contract to legally avoid responsibility.
- D. Have a meeting with the project sponsor to discuss the situation.

Answer: D

Explanation:

The project manager should inform the project sponsor about the issue and seek their guidance and support. The project sponsor is the person who provides the resources and authority for the project, and who can help resolve any conflicts or problems that may arise. The project manager should not withdraw the offer, ignore the lawsuit, or use a third-party company without consulting the project sponsor first, as these actions may have legal, ethical, or financial implications for the project and the organization¹².

NEW QUESTION 31

A developer recommends modifying an existing portion of code that is not part of the scope and is causing low performance on the current solution. Which of the following actions should the project manager most likely take?

- A. Ask a developer to create a change request.
- B. Do nothing because recommendation is scope creep.
- C. Ask a developer to implement the recommendation.
- D. Communicate the change status.

Answer: A

Explanation:

The project manager should ask the developer to create a change request, which is a formal document that describes the proposed change, its benefits, costs, risks, and impacts on the project scope, schedule, budget, and quality. A change request is the first step in the change control process, which involves evaluating, approving, or rejecting changes to the project baselines. The project manager should not do nothing, because ignoring the recommendation could result in poor performance and customer dissatisfaction. The project manager should not ask the developer to implement the recommendation without following the change control process, because that could cause scope creep, which is the uncontrolled expansion of the project scope without proper authorization or adjustment of the project resources and objectives. The project manager should not communicate the change status before the change request is submitted and approved, because that could create confusion and false expectations among the project stakeholders. References = CompTIA Project+ Study Guide: Exam PK0-005, 3rd Edition, Chapter 4: Project Integration Management¹; CompTIA Project+ Certification Study Guide, 3rd Edition, Chapter 4: Project Integration Management²; What is a Change Request and How to Manage It³

NEW QUESTION 36

A project manager needs to ensure that the products produced during the project meet the highest quality standards and that team members understand the importance of these standards. Which of the following should the project manager do?

- A. Train the team members.
- B. Assess the resource pool.
- C. Develop a QA plan.
- D. Create RACI matrix.

Answer: C

Explanation:

A QA plan, or quality assurance plan, is a document that specifies the quality standards, practices, resources, specifications, and activities for a product, service, project, or contract. A QA plan helps to ensure that the products produced during the project meet the highest quality standards and that the project objectives and customer requirements are met. A QA plan also helps to communicate the quality expectations and responsibilities to the team members and other stakeholders, and to monitor and control the quality performance throughout the project. Developing a QA plan is one of the key tasks of the project manager, as it is part of the project scope management and project quality management processes¹²³. References = CompTIA Project+ Study Guide: Exam PK0- 005, 3rd Edition, Chapter 3: Project Scope Management, p. 97; Chapter 5: Project Quality Management, p. 169; 6 Key Steps to Creating A Quality Assurance Plan - The QA Lead; What is Quality Planning? Quality Control Plans | ASQ; What Is A Quality Assurance Plan? - Sofeast

NEW QUESTION 39

When introducing a new information asset, what is the MOST important responsibility of the asset owner?

- A. Information disposal
- B. Information classification
- C. Information access administration
- D. Information backup

Answer: B

Explanation:

The most important responsibility of an asset owner when introducing a new information asset is information classification. This process involves determining the level of sensitivity and the appropriate handling of the asset. Classification helps in applying the right security controls and access permissions, ensuring that the asset is protected according to its value and sensitivity.

References = CompTIA Project+ Certification Study Guide (PK0-005)

NEW QUESTION 44

A project sponsor is struggling to provide the latest project status information on a weekly executive call. Which of the following should be reviewed?

- A. Meeting cadence
- B. Gap analysis
- C. Dashboard
- D. Adoption training

Answer: C

Explanation:

A dashboard is a visual tool that displays key project metrics and indicators in a single view¹². A dashboard can help a project sponsor to provide the latest project status information on a weekly executive call by showing the project progress, budget, schedule, risks, issues, and milestones in a clear and concise way³⁴. A dashboard can also facilitate communication, collaboration, and decision making among project stakeholders⁵⁶. A dashboard should be reviewed and updated regularly to reflect the current state of the project⁷. References = CompTIA Project+ Certification Study Guide⁸, CompTIA Project+ Certification Exam Objectives⁹, Write a Project Status Report in 8 Steps + Template [2023] • Asana⁶, Project Status Reports: 9 Easy Steps & Examples [+ Template]⁷, How To Write a Project Status Report (Definition and Steps)⁸, How to Write a Project Status Report [Template Included] - Toggl⁹, What Is a Project Status? Definition and Key Terms - Indeed¹⁰

NEW QUESTION 48

During a staff meeting, a project manager voices a concern about the client billing rate for a particular engineer. Which of the following documents would the project manager need in order to find this information?

- A. SLA
- B. TOR
- C. SOW
- D. NDA

Answer: C

Explanation:

In order to find the client billing rate for a particular engineer, the project manager would need to refer to the SOW (Statement of Work). The SOW is a document that outlines the work to be performed, the timeframe for completion, and the cost of the project. It also includes information about the resources involved in the project and their billing rates. References: CompTIA Project+ Study Guide Section 2.2.

The project manager would need a statement of work (SOW) to find information about the client billing rate for a particular engineer. A SOW is a document that defines the scope of work for a project or contract. It usually includes information such as deliverables, milestones, timeline, costs, payment terms, quality standards, and acceptance criteria. A SOW can help to specify what services or products will be provided by whom, when, where, how, and for how much.

NEW QUESTION 49

A contractor attended a project meeting that was exclusively for company employees. Which of the following actions should the PM take?

- A. Escalate to vendor management.
- B. Consult the request for proposal.
- C. Review the meeting cadence.
- D. Reinforce the rules of engagement.

Answer: D

Explanation:

The rules of engagement are the guidelines and expectations that define the relationship between the contractor and the company. They may include topics such as communication, confidentiality, access, security, performance, and compliance. The project manager should reinforce the rules of engagement with the

contractor to ensure that they understand and respect the boundaries and protocols of the company. This will help to avoid any potential conflicts, misunderstandings, or breaches of contract. References = CompTIA Project+ Study Guide: Exam PK0-005, 3rd Edition, Chapter 7: Project Stakeholder Management, p. 239; Contractor Rules of Engagement - Cox Enterprises, p. 1; Legal Considerations for Engaging Contractors | LegalVision

NEW QUESTION 54

A project manager has been assigned to a new project. During the planning phase, the project manager needs to get an understanding of the purpose of the project. Which of the following should the project manager do?

- A. Collate the lessons learned.
- B. Perform a gap analysis.
- C. Review existing artifacts.
- D. Conduct a retrospective.

Answer: C

Explanation:

The project manager should review existing artifacts to get an understanding of the purpose of the project. Existing artifacts are documents or records that provide information about the project background, context, scope, objectives, requirements, stakeholders, and deliverables. They may include documents such as project proposal, project charter, business case, feasibility study, statement of work (SOW), or contract. Reviewing existing artifacts can help to clarify the project vision and expectations and provide a basis for planning and executing the project.

NEW QUESTION 58

Which of the following would be considered operational security?

- A. Mobile device compliance
- B. Background screening
- C. Multifactor authentication
- D. Facility access

Answer: D

Explanation:

Operational security (OPSEC) is a process that prevents sensitive information from getting into the wrong hands by viewing operations from the perspective of an adversary¹. Facility access is a form of OPSEC that controls who can enter and exit a physical location where sensitive data or equipment is stored or processed. Facility access can include measures such as locks, alarms, badges, biometrics, guards, and cameras. The other options are not correct because:

? Mobile device compliance is a policy that ensures that mobile devices used by employees or contractors meet certain security standards and requirements, such as encryption, password protection, antivirus, and remote wipe. Mobile device compliance is not a form of OPSEC, but rather a form of data security or device management.

? Background screening is a process that checks the criminal, financial, and employment history of a potential employee or contractor before hiring them. Background screening is not a form of OPSEC, but rather a form of human resource management or risk mitigation.

? Multifactor authentication is a method that requires users to provide two or more pieces of evidence to verify their identity before accessing a system or service, such as a password, a code, a token, or a biometric. Multifactor authentication is not a form of OPSEC, but rather a form of access control or identity management. References = CompTIA Project+ Study Guide: Exam PK0-005, 3rd Edition, Chapter 10: Executing and Closing Projects, page 314; CompTIA Project+ Certification Exam Objectives, Domain 3: Project Execution, Objective 3.2: Given a scenario, execute and monitor project tasks using traditional methodologies; What is Operational Security? The Five-Step Process, Best Practices, and More

NEW QUESTION 63

A project coordinator has started a new project and is reviewing the following characteristics provided by the customer:

- Two developers
- High uncertainty about existing systems
- Risk of frequent requirement changes
- Tight deadlines

Which of the following project methodologies would be best to use in this situation?

- A. PRINCE2
- B. Scrum
- C. SAFe
- D. XP

Answer: B

Explanation:

This answer is based on the best practice of choosing a project management methodology that suits the project characteristics and environment¹². Scrum is an agile framework that is designed to handle complex and uncertain projects with frequent changes and tight deadlines³⁴. Scrum involves a small, cross-functional team that works in short iterations called sprints, delivering incremental and potentially shippable products at the end of each sprint⁵. Scrum also allows for continuous feedback and improvement through daily stand-up meetings, sprint reviews, and retrospectives⁶. Scrum is suitable for this project because it can accommodate the high uncertainty, the risk of requirement changes, and the tight deadlines, while also enabling the two developers to collaborate effectively and deliver value to the customer. References = CompTIA Project+ Certification Study Guide⁷, CompTIA Project+ Certification Exam Objectives⁸, Project Management Methodologies Comparison (11 PM Methods)⁶, Project Management Methodologies: 12 Best Frameworks [2023]⁷, What is Scrum?⁵, Scrum Methodology: The Ultimate Guide⁶

NEW QUESTION 65

A project manager is assigned to a multinational project with team members from different continents. Which of the following is the MOST important aspect for the project manager to consider?

- A. Resource allocation
- B. Communication security
- C. Technological factors
- D. Cultural differences

Answer: D

Explanation:

Cultural differences are the most important aspect for the project manager to consider when assigned to a multinational project with team members from different continents. Cultural differences refer to the variations in beliefs, values, norms, behaviors, customs, and communication styles among people from different countries or regions. Cultural differences can affect how team members interact, communicate, collaborate, negotiate, make decisions, solve problems, manage conflicts, and perform tasks. The project manager should be aware of and respect the cultural differences among team members and foster a positive and inclusive team culture that leverages diversity and promotes trust and cooperation.

NEW QUESTION 68

A PM wants to provide a visual representation of how a project is organized into tasks and how the tasks relate to each other. Which of the following can the PM use?

- A. Milestone chart
- B. Gantt chart
- C. PERT chart
- D. WBS

Answer: B

Explanation:

A gantt chart is a visual representation of a project timeline that shows the tasks, durations, dependencies, and resources of a project in a horizontal bar chart format. A gantt chart can help a project manager to plan, monitor, and control the project progress, scope, and quality. A gantt chart is different from a milestone chart, which only shows the key events or deliverables of a project without the details of the tasks. A gantt chart is also different from a PERT chart, which is a network diagram that shows the logical relationships and sequence of tasks in a project. A gantt chart is also different from a WBS, which is a hierarchical breakdown of the project scope into smaller and manageable components. References = CompTIA Project+ Study Guide: Exam PK0-005, 3rd Edition, Chapter 6: Schedule Management¹; CompTIA Project+ Certification Study Guide, 3rd Edition, Chapter 6: Schedule Management²; What Is a Gantt Chart? 7 Examples for Project Management³; 3 types of visual project management: Timelines, calendars, and boards (with examples)⁴

NEW QUESTION 71

Which of the following BEST describes how an organization should coordinate management of multiple related projects?

- A. Apply the SDLC process.
- B. Establish a program.
- C. Consult the CCB.
- D. Use different frameworks

Answer: B

Explanation:

The BEST way to coordinate management of multiple related projects is to establish a program. A program is a group of related projects that are managed together to achieve specific strategic business objectives. References: CompTIA Project+ Study Guide Section 2.2.1

The organization should establish a program to coordinate management of multiple related projects. A program is a group of related projects, subprograms, and program activities that are managed in a coordinated way to obtain benefits and control not available from managing them individually. A program can help to align multiple projects with strategic goals, optimize resources and risks, and deliver value to stakeholders.

NEW QUESTION 74

During a status meeting for a multisystem program, a program manager learns that some deliverables from another project are delayed. Which of the following should the program manager do next?

- A. Obtain details from the owner of the project.
- B. Update the critical path for the project.
- C. Apply contingency reserves.
- D. Reestimate epic user stories.

Answer: A

Explanation:

The program manager should first obtain details from the owner of the project that is causing the delay, such as the root cause, the impact, the mitigation plan, and the revised timeline. This will help the program manager to assess the situation, communicate with the stakeholders, and adjust the program schedule accordingly. Updating the critical path, applying contingency reserves, and reestimating epic user stories are possible actions that the program manager may take after obtaining the details, depending on the severity and duration of the delay. However, they are not the immediate next steps, as they require more information and analysis. References = CompTIA Project+ Study Guide: Exam PK0-005, Third Edition, Chapter 10: Executing the Project, page 243¹; Dealing with delays - Project Management Institute²

NEW QUESTION 78

A development team, which is working on a software project demonstrates software functionality 10 project stakeholder a week before the implementation date. Several stakeholders comment that the software does not meet the communicated expectations. Which of the following tools should the project manager use to validate the functionality?

- A. Project status report
- B. Requirements Traceability Matrix
- C. Defect log
- D. Signed project charter
- E. Work breakdown structure

Answer: A

NEW QUESTION 82

After determining the appropriate maintenance window, which of the following should occur NEXT in the operational infrastructure change process?

- A. Implement the change.
- B. Approve the test plan.
- C. Notify customers.
- D. Develop a rollback plan.

Answer: D

Explanation:

The project manager should develop a rollback plan next after determining the appropriate maintenance window in the operational infrastructure change process. A rollback plan is a contingency plan that describes how to revert to the previous state of the system or infrastructure in case of a failure or disruption during the change implementation. A rollback plan can help to minimize the impact and risk of the change and ensure business continuity and stability.

NEW QUESTION 87

A system was implemented, and testing was successfully completed. Which of the following should the project manager do NEXT?

- A. Validate against the scope statement and ask for sign-off.
- B. Run a control chart to ensure the quality of the deliverables.
- C. Review the risk register and close up residual risks.
- D. Start the training and handoff for the operations team.

Answer: A

Explanation:

The project manager should validate against the scope statement and ask for sign-off after a system was implemented and testing was successfully completed. The scope statement is a document that defines and documents the project scope, objectives, deliverables, requirements, assumptions, and constraints. The scope statement can help to establish a common understanding and agreement between the project manager and the stakeholders on what the project aims to achieve and deliver. Validating against the scope statement means checking whether the project deliverables meet the agreed-upon scope criteria and quality standards. Asking for sign-off means requesting formal acceptance and approval of the project deliverables from the stakeholders.

NEW QUESTION 88

While working with a contractor, the project manager identified a communication conflict. The contractor did not agree that there was an issue. Which of the following should the project manager and contractor review?

- A. Scope of work
- B. Request for proposal
- C. Vendor rules of engagement
- D. Project schedule

Answer: C

Explanation:

The project manager and contractor should review the vendor rules of engagement, which are the guidelines and expectations for the communication and interaction between the project team and the contractor. The vendor rules of engagement can help to prevent or resolve communication conflicts by clarifying the roles and responsibilities, the frequency and mode of communication, the escalation process, the feedback mechanism, and the performance evaluation criteria of the contractor. The vendor rules of engagement are usually part of the contract or the procurement management plan. The vendor rules of engagement are different from the scope of work, which is the document that describes the work to be performed, the deliverables to be provided, and the acceptance criteria to be met by the contractor. The vendor rules of engagement are also different from the request for proposal, which is the document that solicits proposals from potential contractors by specifying the project requirements, evaluation criteria, and contract terms. The vendor rules of engagement are also different from the project schedule, which is the tool that displays the planned start and finish dates, durations, dependencies, and resources of the project activities and tasks. References = CompTIA Project+ Study Guide: Exam PK0-005, 3rd Edition, Chapter 12: Procurement Management¹; CompTIA Project+ Certification Study Guide, 3rd Edition, Chapter 12: Procurement Management²; Vendor Rules of Engagement³

NEW QUESTION 89

Which of the following communication tools would a project manager use to broadcast information without being assured the information will be received?

- A. Telephone
- B. Videoconference
- C. Face-to-face
- D. Email

Answer: D

Explanation:

Email is a communication tool that allows the project manager to send information to one or more recipients without requiring immediate feedback or confirmation of receipt. Email can be used to broadcast information that is not urgent or critical, such as status updates, meeting minutes, or general announcements¹, p. 75

NEW QUESTION 92

A new project team started work three months ago. The team members are increasing their work productivity and are comfortable asking for help with tasks. Which of the following describes the current stage of the project team?

- A. Performing
- B. Adjourning
- C. Forming
- D. Norming

Answer:

D

Explanation:

The current stage of the project team is norming, which is the third stage of the five stages of team development. In this stage, the team members have resolved their conflicts and differences, and have established a sense of cohesion and collaboration.

They are more productive, supportive, and cooperative, and they follow the agreed norms and rules of the team. They also communicate effectively and seek feedback and assistance from each other. The norming stage is preceded by the forming stage, where the team members get to know each other and the project goals, and the storming stage, where the team members experience disagreements and challenges. The norming stage is followed by the performing stage, where the team members work efficiently and autonomously towards the project outcomes, and the adjourning stage, where the team members complete the project and celebrate their achievements. References = CompTIA Project+ Study Guide: Exam PK0-005, 3rd Edition, Chapter 11: Team Management¹; CompTIA Project+ Certification Study Guide, 3rd Edition, Chapter 11: Team Management²; The 5 Stages of Team Development (Including Examples)³

NEW QUESTION 97

During a sponsor meeting, a PM is assigned to manage a new external project for an IT consultant. The sponsor wants the PM to establish an agreement regarding the exchange of money between both parties. Which of the following documents would the PM most likely create?

- A. Business requirement
- B. Client statement of work
- C. Formal contract
- D. Project charter

Answer: C**Explanation:**

A formal contract is a legal document that defines the terms and conditions of the agreement between the project parties, such as the scope, schedule, budget, quality, deliverables, roles and responsibilities, payment methods, and dispute resolution mechanisms. A formal contract is essential for external projects, especially when there is an exchange of money involved, to protect the interests and rights of both parties and to ensure mutual understanding and compliance. A formal contract is different from a business requirement, which is a statement of the needs and expectations of the customer or stakeholder for the project outcome. A formal contract is also different from a client statement of work, which is a document that describes the work to be performed, the deliverables to be provided, and the acceptance criteria to be met by the project vendor or contractor. A formal contract is also different from a project charter, which is a document that authorizes the project and provides the high-level information about the project objectives, scope, stakeholders, and project manager. References = CompTIA Project+ Study Guide: Exam PK0-005, 3rd Edition, Chapter 4: Project Integration Management¹; CompTIA Project+ Certification Study Guide, 3rd Edition, Chapter 4: Project Integration Management²; 11 Essential Documents To Use as a Project Manager³

NEW QUESTION 99

Which of the following is a reason to use a SOW on a project?

- A. To find out the contact information for the vendors
- B. To review the list of stakeholders
- C. To ensure the team stays within the scope of the contract
- D. To give explicit instruction on how to execute the work

Answer: C**Explanation:**

A statement of work (SOW) is a formal document that defines the entire scope of work involved for a vendor and clarifies deliverables, costs, and timeline¹. It serves as a contractual agreement between a vendor and a client, providing a comprehensive description of the work to be performed². A reason to use a SOW on a project is to ensure the team stays within the scope of the contract, as it outlines what the team will and won't do on a project, saving from painful client negotiations and protecting the timeline and the bottom line³. References = CompTIA Project+ PK0-005 Certification Study Guide, Chapter 3: Initiating Projects Part 1, page 63; What Is a Statement of Work? Definition & Examples, Introduction and What Is a Statement of Work (SOW) In Project Management? sections; Statement Of Work Ultimate Guide: Simple Definition & Template, Introduction and What is a Statement of Work? sections; What Is a Statement of Work (SOW)? - Coursera, Introduction section.

NEW QUESTION 101

A company needs to have structured cabling installed in one of its buildings. Which of the following would be the best document for the company to use to obtain and compare information on cabling services and costs from various vendors?

- A. RFB
- B. RFQ
- C. RFI
- D. RFP

Answer: D**Explanation:**

A request for proposal (RFP) is the best document for the company to use in this scenario, because it is the most detailed and personalized type of request document. An RFP allows the company to specify the project scope, requirements, deliverables, evaluation criteria, and budget for the structured cabling installation, and to solicit proposals from various vendors that can meet those needs. An RFP also enables the company to compare the vendors based on their qualifications, experience, methodology, and pricing, and to select the best one for the project. An RFP is more suitable than an RFB, RFQ, or RFI, because those documents are less comprehensive and more generic, and they do not provide enough information for the company to make an informed decision. References = CompTIA Project+ Study Guide: Exam PK0-005, Third Edition, Chapter 5: Initiating the Project, page 1131; RFI, RFP, RFQ: Understanding the Differences²; Data Center Structured Cabling RFP Template³

NEW QUESTION 104

Which of the following is a typical characteristic of Scrum?

- A. Large teams
- B. Low-risk scope

- C. Self-organized team
- D. Well-defined scope

Answer: C

Explanation:

A self-organized team is a typical characteristic of Scrum, which is an agile framework for managing complex projects. A self-organized team is a group of motivated and skilled individuals who have the autonomy and authority to make decisions and collaborate on how to deliver the project goals. A self-organized team does not rely on a manager or a leader to assign tasks, monitor progress, or resolve issues. Instead, a self-organized team uses Scrum events, such as daily stand-ups, sprint planning, sprint review, and sprint retrospective, to coordinate their work, communicate with each other, and inspect and adapt their process and product¹²³. References = CompTIA Project+ Study Guide: Exam PK0-005, 3rd Edition, Chapter 2: Project Methodologies, p. 55; Scrum Characteristics - Scrumversity; What is Scrum? | Scrum.org; Characteristics of a Great Scrum Team | Scrum.org

NEW QUESTION 106

Which of the following best represents the project impact to a company's brand value?

- A. The project is compliant with local and state laws and becomes the standard for new projects.
- B. The project promotes new initiatives to expand its benefit to other communities.
- C. The project exceeds the sales quota for the third quarter and raises the bar for next periods. The project meets the expected milestones and finishes on time and within budget.

Answer: B

Explanation:

the brand of a project should deliver the message about its value and goals, and a proper brand helps the project get the necessary support and increases loyalty. The project that promotes new initiatives to expand its benefit to other communities is the one that best represents the project impact to a company's brand value, as it shows the company's vision, cause, and reputation.

NEW QUESTION 110

Which of the following is required to provide a hardware installation with a Tier 5 redundancy level?

- A. Storage project
- B. Computer services project
- C. Database project
- D. Multitiered architecture project

Answer: D

Explanation:

A multitiered architecture project is a type of project that involves designing and implementing a system that consists of multiple layers or tiers, such as presentation, application, and data. A multitiered architecture project can provide a high level of redundancy, scalability, and performance, as each tier can have multiple servers or components that can handle requests and failures independently. A Tier 5 redundancy level is the highest level of redundancy that requires a fully redundant, mirrored system plus one additional backup unit for every component¹².

NEW QUESTION 114

A project team is developing an application that will allocate a building's parking spaces. The building owner does not agree with using corporate colors in the application and has blocked the release of the beta version for testing. Which of the following best describes what the project manager should have done in the initiation phase to prevent this issue?

- A. Review of existing artifacts
- B. Development of an issue log
- C. Identification and assessment of stakeholders
- D. Establishment of accepted communication channels

Answer: C

Explanation:

The project manager should have identified and assessed the building owner as a key stakeholder in the initiation phase, and understood their expectations and requirements for the application. This would have helped to avoid the conflict over the corporate colors and the delay in testing. Stakeholder identification and assessment is an important process in the initiation phase, as it helps to define the project scope, objectives, and success criteria, and to establish a communication plan¹². References = CompTIA Project+ PK0-005 Certification Study Guide,

NEW QUESTION 118

Someone claiming to be from a tax agency sent an email to a team member asking for access to the project repository. Which of the following BEST describes this scenario?

- A. Social engineering
- B. Phishing
- C. Spoofing
- D. Hacking

Answer: B


Explanation:

Phishing is a scenario where someone claiming to be from a legitimate organization sends an email or other message to a target person asking for sensitive information or access to a system or account. Phishing is a type of cyberattack that aims to trick the target into revealing personal or financial data or installing malware on their device. Phishing can compromise the security and privacy of the target and expose them to identity theft, fraud, or other malicious activities.


NEW QUESTION 122

An IT intern was assigned to set up workstations as part of a project. The IT intern was very careful to do the task well and initially referred to notes while performing the task. By the end of the two-week rotation, the IT intern no longer needed the notes and completed more set-ups in less time. Which of the following MOST likely represents the observed relationship in this scenario?


A)

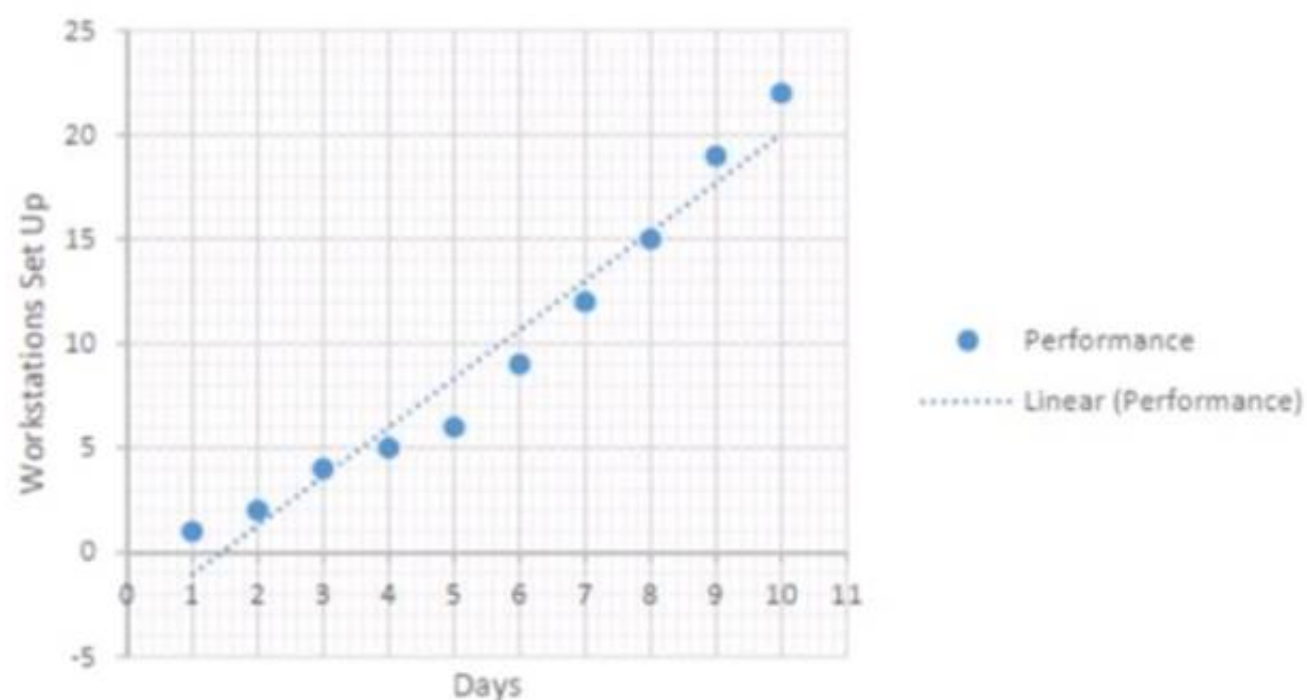


B)

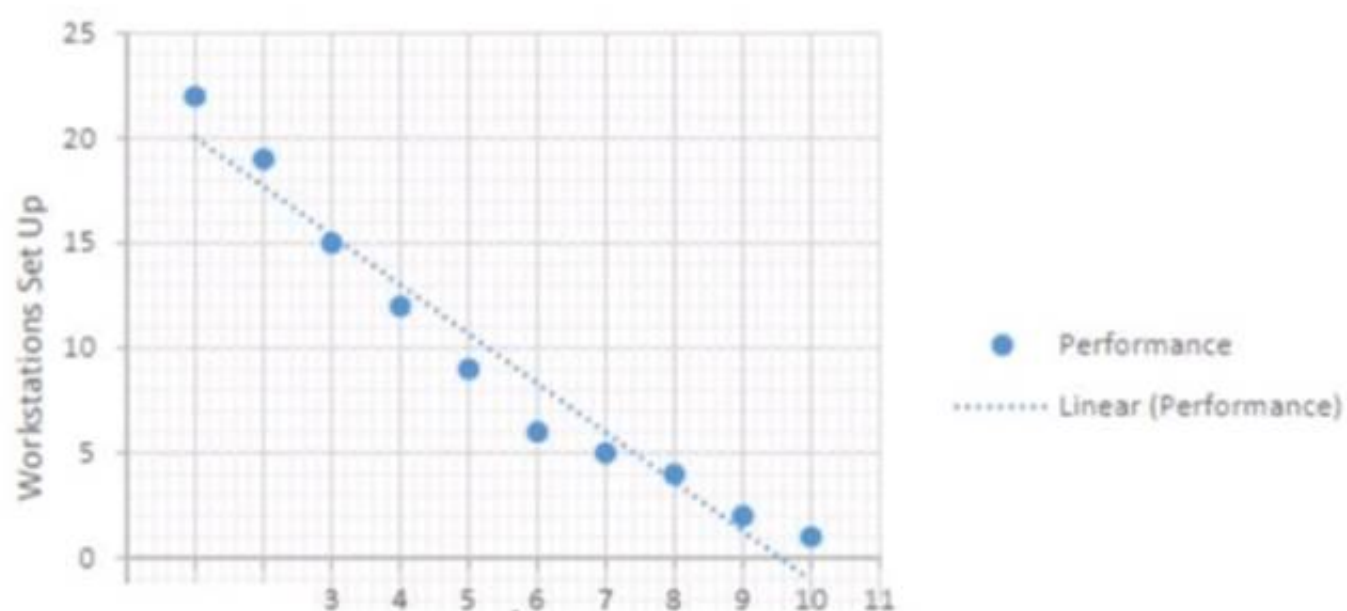

C)

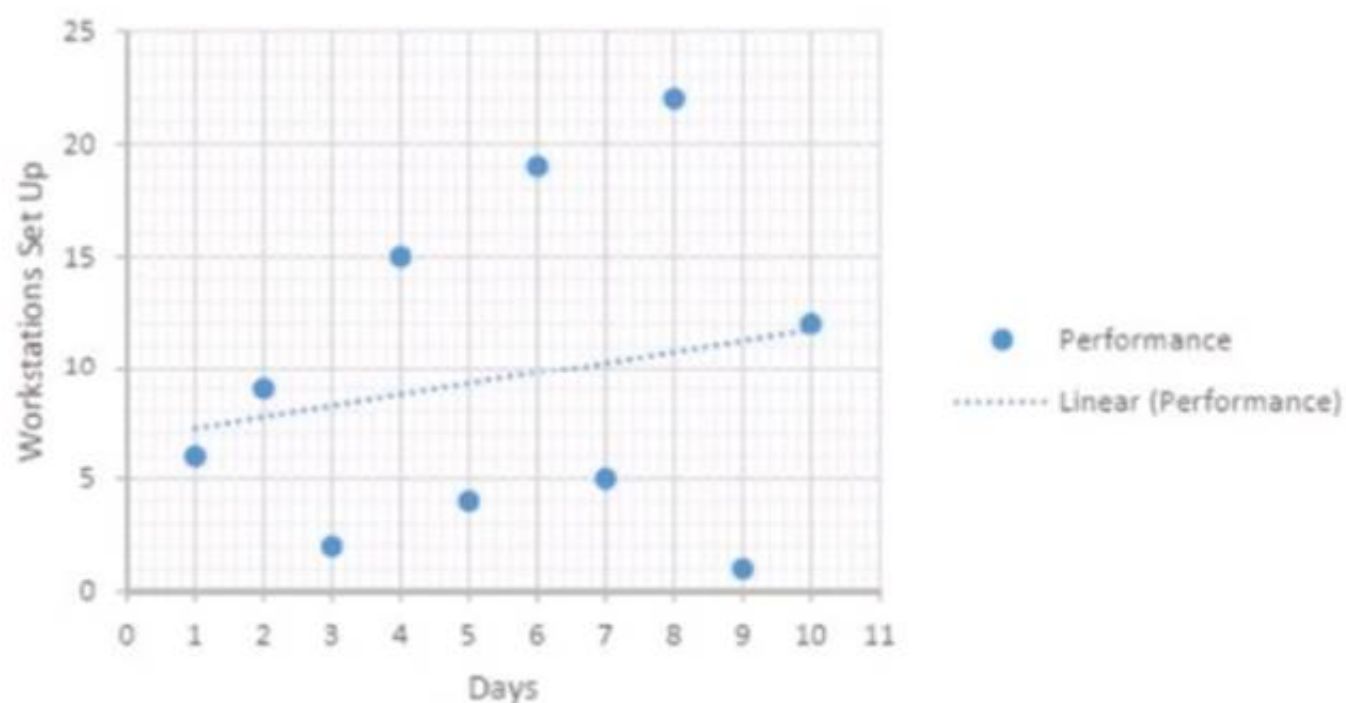

D)

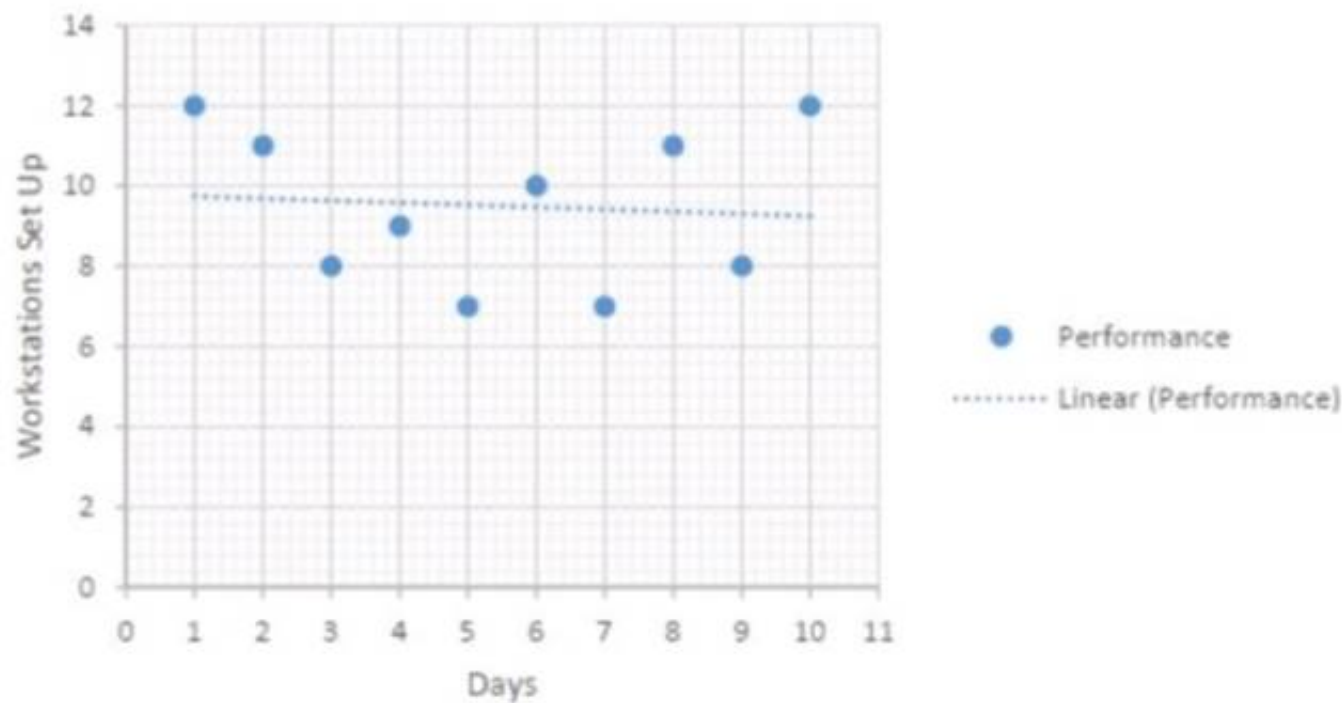

- A. Option A
- B. Option B
- C. Option C
- D. Option D

Answer: C

Explanation:

Option C shows a graph that most likely represents the observed relationship in this scenario. The graph shows a learning curve, which is a graphical representation of the relationship between a learner's performance on a task and the number of attempts or time required to complete the task. The learning curve theory proposes that a learner's efficiency in a task improves over time the more the learner performs the task. In this case, the IT intern was able to complete more set-ups in less time as they gained more experience and proficiency over the two-week rotation¹²

NEW QUESTION 124

Which of the following activities are performed during the closing phase? (Select three).

- A. Requesting project charter sign-off
- B. Recognizing project team efforts and rewarding team members
- C. Working with the financial team to obtain return of investment
- D. Revoking resource credentials from the system
- E. Updating the risk register with new findings
- F. Informing the functional manager about the release of resources
- G. Monitoring project team performance

Answer: BDF

Explanation:

The closing phase of a project involves finalizing all project activities, delivering the project deliverables, releasing the project resources, and closing out the project accounts. Some of the activities that are performed during this phase are¹²:

- Recognizing project team efforts and rewarding team members. This is an important activity to acknowledge the contributions of the project team, celebrate the project success, and motivate the team members for future projects. Recognition and rewards can be given in various forms, such as certificates, bonuses, gifts, or feedback.
- Revoking resource credentials from the system. This is a security measure to ensure that the project resources, such as staff, contractors, vendors, or consultants, do not have access to the project systems, data, or assets after the project is completed. Revoking credentials can prevent unauthorized access, data breaches, or misuse of project resources.
- Informing the functional manager about the release of resources. This is a communication activity to notify the functional manager, who is responsible for the allocation and management of resources, that the project resources are no longer needed and can be reassigned to other projects or tasks. Informing the functional manager can help to optimize the resource utilization, avoid resource conflicts, and plan for future resource needs.

References = CompTIA Project+ PK0-005 Certification

NEW QUESTION 129

A project manager has been very diligent in maintaining the version control for the documentation of requirements. Which of the following tools is the project manager using?

- A. Multiauthoring software
- B. Word processor
- C. Real-time polling
- D. Conferencing platforms

Answer: A

Explanation:

The project manager is using multiauthoring software to maintain the version control for the documentation of requirements. Multiauthoring software is a type of software that allows multiple users to create, edit, and collaborate on documents simultaneously. It also provides features such as tracking changes, commenting, reviewing, and merging versions. Multiauthoring software can help to improve the quality, accuracy, and consistency of documents and facilitate communication and feedback among stakeholders. Examples of multiauthoring software include Google Docs, Microsoft Word Online, and Confluence³⁴

NEW QUESTION 132

A project manager is reviewing a signed legal document pertaining to the hiring of a vendor who will develop an experimental solution. The vendor could not provide accurate estimates at this time because the requirements will probably be changing. The document also contains information about the resources involved and the rates the vendor will charge for the work. Which of the following best describes the legal document the project manager is reviewing?

- A. Time and materials contract
- B. Master service agreement
- C. Fixed-price contract
- D. Non-disclosure agreement

Answer: A

Explanation:

A time and materials contract is a type of contract where the buyer pays the seller for the actual time and materials used during the project. This type of contract is suitable when the scope of work is uncertain or likely to change, and the vendor cannot provide accurate estimates. The document also specifies the resources involved and the rates the vendor will charge for the work¹².

NEW QUESTION 133

Which of the following is a consideration when determining a project's ESG factors?

- A. Project management methodology
- B. IT infrastructure security
- C. Proper accounting practices
- D. Corporate values compliance

Answer: D

Explanation:

Corporate values compliance is a consideration when determining a project's ESG factors, because it reflects how a project aligns with the ethical standards and social responsibility of the organization. Corporate values compliance can help to enhance the reputation, trust, and loyalty of the organization among its stakeholders, as well as to avoid legal or regulatory issues that may arise from violating the values. Corporate values compliance can also influence the project scope, objectives, deliverables, and stakeholders, as well as the project management methodology, processes, and practices. The other options are not directly related to ESG factors. Project management methodology is the approach or framework that guides how a project is planned, executed, monitored, and controlled. IT infrastructure security is the protection of the hardware, software, network, and data components of a project from unauthorized access, use, modification, or destruction. Proper accounting practices are the rules and standards that govern how financial transactions and statements are recorded, reported, and audited for a project. References = CompTIA Project+ Study Guide: Exam PK0-005, 3rd Edition, Chapter 5: Project Scope Management¹; CompTIA Project+ Certification Study Guide, 3rd Edition, Chapter 5: Project Scope Management²; What Is Environmental, Social, and Governance (ESG) Investing

NEW QUESTION 135

Two team members have a minor disagreement on how a task should be performed. The project manager plans to meet with the team members to discuss the matter. Which of the following techniques should the project manager use to emphasize the areas of agreement and downplay the opposing views?

- A. Compromising
- B. Forcing
- C. Smoothing
- D. Collaborating

Answer: C

Explanation:

Smoothing is a conflict resolution technique that involves minimizing or ignoring the differences between the parties and focusing on the common interests or goals¹. It is often used when the conflict is not very important or when there is a need to maintain harmony and relationships². By using smoothing, the project manager can reduce the tension and stress caused by the disagreement and encourage the team members to cooperate and work together. Smoothing is different from compromising, which involves finding a middle ground or a trade-off that partially satisfies both parties; forcing, which involves imposing one's own solution or decision on the other party; and collaborating, which involves finding a win-win solution that fully satisfies both parties³. References = CompTIA Project+ PK0-005 Certification Study Guide, Chapter 10: Executing Projects Part 1, page 297; A Quick Guide to Resource Smoothing: Definition, Benefits, and Process, Conflict Resolution Techniques section; Resource Smoothing: How To Use In Project Management | Hive, Smoothing section.

NEW QUESTION 136

Following a successful release, a project manager sent a survey to all stakeholders to gain an understanding of opportunity areas for the team. Which of the following can use the survey results as an input?

- A. Daily stand-up
- B. Project momentum
- C. Performance feedback
- D. Meeting minutes

Answer: C

Explanation:

The project manager can use the survey results as an input for performance feedback for the project team members. Performance feedback is a process of providing constructive and timely information on the performance of individuals or teams in relation to project goals and expectations. Performance feedback can help to motivate, improve, and recognize project team members³⁴⁵.

The survey results can be used as an input for performance feedback. Performance feedback involves analyzing and evaluating the performance of the project team and project management against the project plan, including identifying areas for improvement. The survey results can help identify these areas for improvement and provide feedback to the project team on their performance. References: CompTIA Project+ Study Guide Section 4.1.1

NEW QUESTION 138

A project manager makes a company-wide announcement about the successful completion of a project and thanks team members. Which of the following is the project manager doing?

- A. Bringing attention to the project sponsor
- B. Sharing lessons learned
- C. Collecting feedback
- D. Celebrating the team's hard work

Answer: D

Explanation:

A project manager who makes a company-wide announcement about the successful completion of a project and thanks team members is doing the following: Celebrating the team's hard work: This is the correct answer, as the project manager is acknowledging the efforts and contributions of the team members and showing appreciation and recognition for their performance¹².

Bringing attention to the project sponsor: This is not the correct answer, as the project manager is not highlighting the role or involvement of the project sponsor, who is the person who provides the resources and authority for the project.

Sharing lessons learned: This is not the correct answer, as the project manager is not discussing the successes, challenges, or best practices of the project, which are part of the lessons learned process.

Collecting feedback: This is not the correct answer, as the project manager is not soliciting any input or opinions from the team members or other stakeholders, which are part of the feedback process.

NEW QUESTION 141

A PM is working on the preliminary scope statement and identifies that this project has the same approach as another project that was completed last year. Which of the following actions would the PM most likely perform?

- A. Call the previous PM for advice on risks and issues.
- B. Ask the project sponsor to provide previous final project report results.
- C. Complete the project charter using the other PM's subject matter expertise.
- D. Use existing artifacts and accommodate based on the current project success criteria.

Answer: D

Explanation:

This answer is based on the best practice of using historical information and lessons learned from previous projects to improve the planning and execution of current projects¹². By using existing artifacts, such as scope statements, project plans, risk registers, and change logs, the PM can leverage the knowledge and experience of the previous PM and avoid repeating the same mistakes or oversights. However, the PM should also accommodate the artifacts based on the current project success criteria, which may differ from the previous project in terms of scope, schedule, budget, quality, or stakeholder expectations³⁴. The PM should not rely solely on the previous PM's advice, the project sponsor's report, or the project charter, as these sources may not provide enough detail or accuracy for the current project's scope statement. References = CompTIA Project+ Certification Study Guide⁵, CompTIA Project+ Certification Exam Objectives⁶, How to Use Historical Information in Project Management¹, How to Use Lessons Learned to Improve Project Management², How to Define Project Success Criteria³, How to Use Existing Artifacts in Project Management⁴

NEW QUESTION 142

A project manager and team are currently in the planning phase of a project. Which of the following should the team do during this phase?

- A. Identify and assess stakeholders.
- B. Hold daily status meetings.
- C. Remove access and plan the project sign-off.
- D. Review assumptions and constraints for input to the risk register.

Answer: D

Explanation:

The project manager and team should review assumptions and constraints for input to the risk register during the planning phase of a project. Assumptions are statements that are considered to be true for the purpose of planning, but may or may not be valid in reality. Constraints are factors that limit the project scope, time, cost, quality, or resources. Both assumptions and constraints can introduce risks to the project, which are uncertain events or conditions that can have a positive or negative impact on the project objectives. The risk register is a document that records the identified risks, their causes, impacts, probabilities, responses, owners, and status. Reviewing assumptions and constraints can help the project manager and team identify, analyze, prioritize, and plan for the potential risks that may affect the project¹².

The other options are not the correct activities that the team should do during the planning phase of a project. Identifying and assessing stakeholders (option A) is an activity that is done during the initiating phase of a project, not the planning phase. Stakeholders are individuals or groups that have an interest or influence in the project, and their identification and assessment is important to define the project scope, objectives, and success criteria, and to establish a communication plan¹². Holding daily status meetings (option B) is an activity that is done during the executing and monitoring and controlling phases of a project, not the planning phase. Daily status meetings are short and frequent meetings where the project team members report on their progress, issues, and plans for the next day. Daily status meetings can help the project manager track the project performance, resolve problems, and communicate updates¹². Removing access and planning the project sign-off (option C) is an activity that is done during the closing phase of a project, not the planning phase. Removing access is a security measure to ensure that the project resources do not have access to the project systems, data, or assets after the project is completed. Planning the project sign-off is a process to obtain the formal acceptance and approval of the project deliverables from the stakeholders and customers¹².

NEW QUESTION 143

During the execution phase, user accepted testing failed; nonetheless, the vendor PM is insisting that the program manager approve the invoice for this phase. Which of the following actions should the Program manager take?

- A. Escalate the issue with the project sponsor and ask for assistance in managing the situation.
- B. Work with the vendor to achieve a compromise that benefits everyone.
- C. Approve the invoice to avoid damaging the relationship with the vendor.
- D. Schedule a call with the vendor PM and vendor executive to review the statement of work.

Answer: D

Explanation:

The program manager should schedule a call with the vendor PM and vendor executive to review the statement of work (SOW), which is a document that defines the scope, deliverables, timeline, quality, and payment terms of the project. The program manager should clarify the expectations and criteria for user acceptance testing (UAT), which is a process of verifying that the system meets the user's requirements and expectations. The program manager should also discuss the reasons for the UAT failure and the corrective actions needed to resolve the issues. The program manager should not approve the invoice until the UAT is successfully completed, as this would compromise the quality and value of the project. The program manager should also not escalate the issue or work on a compromise without first reviewing the SOW and communicating with the vendor¹².

NEW QUESTION 144

A project manager is eager to define access requirements during the initiation phase of a project. Which of the following steps should the project manager perform first?

- A. Define the WBS.
- B. Develop a RAM.
- C. Manage the vendors.
- D. Assess the resource pool.

Answer: D

Explanation:

This answer is based on the best practice of defining access requirements in project management, which is to identify the roles, responsibilities, and permissions of the project team members and other stakeholders who need to access the project information, resources, and deliverables¹². The first step in this process is to assess the resource pool, which is the availability and capability of the human resources that can be assigned to the project³⁴. By assessing the resource pool, the project manager can determine the skills, experience, and security clearance of the potential project team members, as well as their reporting relationships, communication preferences, and expectations⁵⁶. This information can help the project manager to define the access requirements for each role and stakeholder group, and to assign the appropriate level of access to the project data, documents, tools, and systems⁷⁸. References = CompTIA Project+ Certification Study Guide⁹, CompTIA Project+ Certification Exam Objectives¹⁰, What is Requirements Management?, How to Write Project Requirements, A Guide to Functional Requirements, Project Requirements Management: A Quick Guide, Creating clear project requirements, How to Define Project Roles and Responsibilities

NEW QUESTION 149

Which of the following offers administrators more direct control over operating systems?

- A. Infrastructure as a service
- B. Software as a service
- C. Functions as a service
- D. Platform as a service

Answer: A

Explanation:

Infrastructure as a service (IaaS) offers administrators more direct control over operating systems than other cloud service models. IaaS is a type of cloud computing service that provides virtualized computing resources such as servers, storage, network, and operating systems over the internet. IaaS allows users to rent or lease infrastructure resources on demand and pay only for what they use. IaaS gives users more flexibility and control over their infrastructure resources and enables them to configure, manage, and customize their operating systems according to their needs and preferences³

NEW QUESTION 151

Because the project team lacks hands-on experience, the project manager has decided to involve a third-party vendor to complete the development of a product. Which of the following documents should the project manager expedite first?

- A. RFI
- B. RFP
- C. RFQ
- D. RFB

Answer: B

Explanation:

When a project team lacks hands-on experience and decides to involve a third-party vendor for product development, the first document to expedite is a Request for Proposal (RFP). An RFP outlines the project requirements and asks potential vendors to submit proposals detailing how they would meet those requirements and at what cost. This allows the project manager to evaluate the capabilities and offerings of different vendors before making a decision.

References = CompTIA Project+ Certification Study Guide (PK0-005)

NEW QUESTION 156

Which of the following is the main reason for documenting artifacts?

- A. To provide a record of the project's progress and achievements for future reference
- B. To show stakeholders that the project is on track and progressing as planned
- C. To help team members be aware of roles and responsibilities
- D. To ensure that the project team understands the importance of the project to the organization

Answer: A

Explanation:

Documenting artifacts is the main reason for creating and maintaining project documents that relate to the management of the project, not the project deliverables. Artifacts are used to define, support, and align the project work to the project requirements and business goals. They also serve as a source of information and evidence for future projects, audits, reviews, and lessons learned¹. Documenting artifacts helps to capture the project's history, performance, outcomes, and best practices, which can be useful for organizational learning and improvement².

References = CompTIA Project+ PK0-005 Certification Study Guide, Chapter 14: Closing the Project, page 403; Project Artifacts and How to Use Them - Rebel's

Guide to Project Management, Introduction and What are project artifacts in project management? sections; Project Management Artifacts: Definition, Types, and Phases, Introduction and What are project artifacts in project management? sections.

NEW QUESTION 161

A PM received feedback from the project sponsor that the resources involved in the project are unsure of their daily activities. Which of the following is the MOST effective step for the PM to take to ensure clarity within the team?

- A. Create a list of tasks and share it with the team.
- B. Resend the scope of work to the team.
- C. Review the Gantt chart weekly with the team.
- D. Have the project sponsor meet with the team.

Answer: C

Explanation:

Reviewing the Gantt chart weekly with the team would be the most effective step for the project manager to take to ensure clarity within the team after receiving feedback from the project sponsor that the resources involved in the project are unsure of their daily activities. A Gantt chart is a graphical tool that shows the schedule of a project, including the start and end dates, durations, dependencies, milestones, and progress of each task or activity. Reviewing the Gantt chart weekly with the team can help to clarify their roles and responsibilities, assign tasks and deadlines, track and report their status and performance, identify and resolve any issues or risks, and keep them aligned and engaged with the project goals.VVVVVVVVVVVVVV

NEW QUESTION 163

A project manager needs to update the project sponsor and senior stakeholders about the progress of a project. Which of the following tools will the project manager MOST likely use?

- A. Dashboard
- B. Gantt chart
- C. Work breakdown structure
- D. Requirements Traceability Matrix

Answer: A

Explanation:

A dashboard is a tool that the project manager will most likely use to update the project sponsor and senior stakeholders about the progress of a project. A dashboard is a graphical tool that displays key performance indicators (KPIs), metrics, and data related to a project using charts, graphs, tables, or other visual elements. A dashboard can help to provide a quick and easy overview of the project status and performance and highlight any issues or risks that need attention.

NEW QUESTION 167

During the testing phase of a project, the regression test fails due to a specific item that is disrupting the entire system. Which of the following documents should the project manager use to identify who requested this item?

- A. Issue log
- B. Risk register
- C. Defect log
- D. Traceability matrix

Answer: D

Explanation:

A traceability matrix is a document that maps the requirements of a project to the deliverables, test cases, and changes that are produced to meet those requirements. It helps the project manager to track the origin, status, and impact of each requirement throughout the project life cycle. A traceability matrix can also identify who requested or approved each requirement. Therefore, the project manager can use the traceability matrix to identify who requested the specific item that caused the regression test to fail12.

NEW QUESTION 170

A PM has identified all the resources involved in a project. The next step is to identify which resources are responsible for which tasks. Which of the following should be used to document this information?

- A. RFI
- B. RACI
- C. WBS
- D. SOW

Answer: B

Explanation:

The RACI (Responsible, Accountable, Consulted, Informed) matrix is used to document which resources are responsible for which tasks. The RACI matrix is a tool that helps to clarify roles and responsibilities on a project. It assigns a level of responsibility to each resource involved in the project. References: CompTIA Project+ Study Guide Section 3.4.

The project manager should use a RACI matrix to document which resources are responsible for which tasks. A RACI matrix is a type of responsibility assignment matrix

(RAM) that plots the roles and responsibilities of resources on a project team. RACI stands for Responsible, Accountable, Consulted, and Informed. A RACI matrix can help to clarify who does what on a project, avoid confusion and duplication of work, and improve communication and collaboration among team members.

NEW QUESTION 173

A stakeholder raises a concern with a project manager because of the number of emails that have been received before a coding release. Which of the following actions should the project manager take next?

- A. Inform the CCB to stop communication.
- B. Establish a RACI matrix.
- C. Escalate the communication issues.
- D. Revise the communication plan.

Answer: D

Explanation:

When stakeholders express concerns about the volume of communication, it's important to review and adjust the communication plan to ensure it meets the project's needs and stakeholders' preferences. A RACI matrix is useful for defining roles and responsibilities but does not address communication frequency or methods directly. Escalating the issue may not be necessary if it can be resolved by revising the plan. Informing the CCB (Change Control Board) to stop communication is not advisable as the CCB's role is to oversee changes, not to manage day-to-day communications. References = The CompTIA Project+ Certification Study Guide provides detailed information on managing the project life cycle, establishing communication plans, and handling stakeholder concerns¹.

NEW QUESTION 174

Which of the following requires the MOST availability from the business team?

- A. SDLC
- B. Scrum
- C. PRINCE2
- D. Waterfall

Answer: B

Explanation:

Scrum requires the most availability from the business team among the given options. Scrum is a popular agile framework that organizes work into short iterations called sprints, usually lasting one to four weeks. Scrum emphasizes collaboration between teams, customers, and stakeholders and encourages open communication and transparency throughout the project lifecycle. Scrum requires frequent involvement and feedback from the business team through activities such as product backlog refinement, sprint planning, sprint review, sprint retrospective, and daily scrum meetings.

NEW QUESTION 176

Which of the following software programs would be BEST to use to store information related to business transactions?

- A. Record management system
- B. Customer relationship management
- C. Enterprise resource planning
- D. Content management system

Answer: B

Explanation:

Customer relationship management (CRM) software would be the best to use to store information related to business transactions. CRM software is a type of software that helps businesses manage their interactions and relationships with current and potential customers. CRM software can store and organize information such as customer contact details, purchase history, preferences, feedback, complaints, etc. CRM software can help businesses improve customer service, satisfaction, loyalty, retention, and revenue ¹

NEW QUESTION 179

A project manager is receiving reports of the actual project expenditures and, based on this information, is making adjustments to the budget. In which of the following phases does this occur?

- A. Planning
- B. Closure
- C. Initiation
- D. Execution

Answer: D

Explanation:

The execution phase is when the project manager and the team execute the project plan, deliver the project outputs, and monitor and control the project performance. This includes tracking and managing the project budget, scope, schedule, quality, and risks. Making adjustments to the budget based on the actual project expenditures is part of the monitoring and controlling process in the execution phase. References = CompTIA Project+ Study Guide: Exam PK0-005, 3rd Edition, Chapter 10: Executing and Closing Projects, p. 263.

NEW QUESTION 182

A project team participates in a brainstorming session to define the guidance, direction, and approach for monitoring established procedures for developed products. Which of the following plans is the team creating?

- A. Project transition
- B. Project management
- C. Project communications
- D. Project quality assurance

Answer: D

Explanation:

Project quality assurance is the process of ensuring that the project meets the quality standards and requirements defined by the stakeholders and the organization. It involves planning, implementing, and monitoring quality activities throughout the project life cycle. Project quality assurance is different from project

quality control, which is the process of inspecting and testing the project deliverables and outputs to identify and correct defects. Project quality assurance is also different from project transition, which is the process of transferring the project deliverables and outputs to the end users or customers. Project management is the application of knowledge, skills, tools, and techniques to project activities to meet the project objectives. Project communications is the process of planning, creating, distributing, and managing information among the project stakeholders. References = CompTIA Project+ Study Guide: Exam PK0-005, 3rd Edition, Chapter 8: Quality Management¹; CompTIA Project+ Certification Study Guide, 3rd Edition, Chapter 8: Quality Management²

NEW QUESTION 187

A team is working on a project that has different stages, such as initiation, planning, execution, and closure. Which of the following is this an example of?

- A. Agile
- B. Waterfall
- C. Standard
- D. Hybrid

Answer: B

Explanation:

The waterfall methodology is a project management framework that follows a linear and sequential process, where each stage of the project must be completed before moving on to the next one. The stages of the waterfall model are initiation, planning, execution, and closure, as described in the question¹².

NEW QUESTION 190

A risk management team for a software project decided to outsource the development of a specific portion of a system due to a lack of internal resources. Which of the following risk responses does this demonstrate?

- A. Avoid
- B. Transfer
- C. Accept
- D. Share

Answer: B

Explanation:

Outsourcing the development of a system component due to a lack of internal resources is a risk response strategy known as 'transfer.' This approach shifts the risk to a third party who will now be responsible for managing that portion of the project. It is commonly used when an organization does not have the expertise or capacity to handle specific risks internally.

References = The answer is based on standard project management practices and the typical use of risk response strategies in the field. For detailed information, please refer to the CompTIA Project+ Study Guide and other official CompTIA resources.

NEW QUESTION 191

Which of the following would be best to utilize when managing communications for project teams across multiple time zones?

- A. Business collaboration tool
- B. Email
- C. Virtual meetings
- D. Enterprise CMS

Answer: A

Explanation:

A business collaboration tool is a software that enables teams to communicate, share, and create together online. A business collaboration tool can help project teams across multiple time zones to overcome the challenges of distance, time differences, and cultural diversity. A business collaboration tool can provide features such as instant messaging, video conferencing, file sharing, document editing, project management, and more. A business collaboration tool can also integrate with other applications and platforms that the project team uses. A business collaboration tool can improve the efficiency, productivity, and quality of the project team's work¹². References = CompTIA Project+ Study Guide: Exam PK0-005, 3rd Edition, Chapter 4: Project Communications, p. 137; The 15 best collaboration tools for productive teams - Workable; 17 Best Business Collaboration Tools for Teams - Venngage

NEW QUESTION 193

A project team needs a tool to store information that is captured throughout the life cycle of a project. The information should be stored in a centralized location that is easily accessible to all stakeholders and will provide search functionality. Which of the following tools should be used?

- A. Secure folder
- B. Real-time, multiauthoring editing software
- C. Digital whiteboard
- D. Wiki knowledge base

Answer: D

Explanation:

A wiki knowledge base is a tool that allows the project team to store, organize, and share information that is captured throughout the life cycle of a project. A wiki knowledge base is stored in a centralized location that is easily accessible to all stakeholders via a web browser. A wiki knowledge base also provides search functionality that enables the users to find the information they need quickly and easily. A wiki knowledge base can help the project team to document the project requirements, scope, schedule, budget, quality, risks, issues, lessons learned, and best practices.

A wiki knowledge base is different from a secure folder, which is a tool that protects the files and folders from unauthorized access or modification. A secure folder may not be easily accessible to all stakeholders, and may not provide search functionality or collaboration features. A wiki knowledge base is also different from a real-time, multiauthoring editing software, which is a tool that allows the project team to create and edit documents simultaneously and synchronously. A real-time, multiauthoring editing software may not be suitable for storing large amounts of information, and may not provide the same level of organization and structure as a wiki knowledge base. A wiki knowledge base is also different from a digital whiteboard, which is a tool that allows the project team to brainstorm, visualize, and communicate ideas. A digital whiteboard is not designed for storing information, and may not provide the same level of search functionality or security as a wiki knowledge base. References = CompTIA Project+ Study Guide: Exam PK0-005, 3rd Edition, Chapter 3: Project Communications Management¹; CompTIA

NEW QUESTION 197

A PM is working on a strategy to store records. Which of the following dements must be included in this plan? (Select TWO)

- A. Data management
- B. Issue management
- C. Work breakdown structure
- D. Document management
- E. Communication management
- F. Risk management


Answer: AD

Explanation:

A strategy to store records must include data management and document management as two essential elements. Data management is the process of ensuring that the data collected, stored, and used by the project is accurate, complete, consistent, secure, and accessible. Data management helps to maintain the quality and integrity of the project data and supports the analysis and reporting of the project outcomes¹, p. 4 Document management is the process of creating, organizing, storing, retrieving, and disposing of project documents in a systematic and controlled way. Document management helps to ensure that the project documents are available, reliable, usable, and authentic throughout the project life cycle and beyond. Document management also helps to comply with the legal, regulatory, and organizational requirements for records retention and disposition², p. 3

NEW QUESTION 199

During a brainstorming session, a project team is elaborating on what caused the unexpected crash of the website that the team was developing. Given the following:

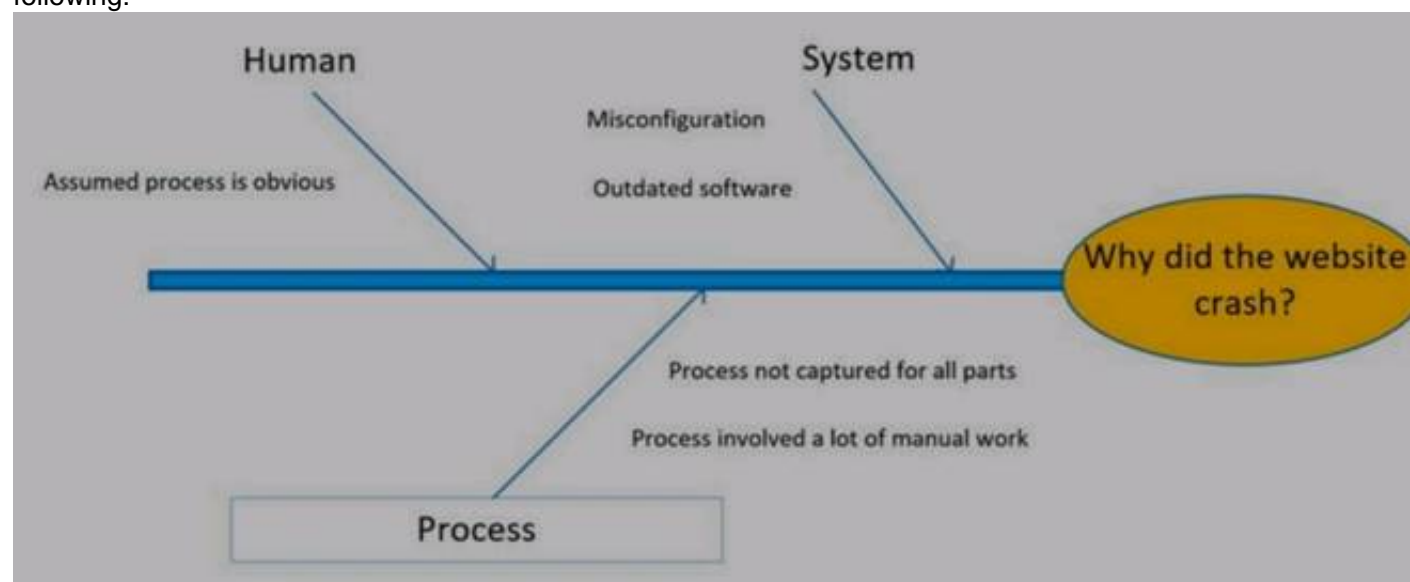

Which of the following was the initial cause of the issue?

- A. Inadequate memory
- B. Incorrect configuration
- C. Lack of infrastructure
- D. Inadequate instructions

Answer: B

Explanation:

Incorrect configuration was the initial cause of the issue that caused the unexpected crash of the website that the team was developing. The diagram given is an example of a fishbone diagram or a cause-and-effect diagram that shows the possible causes of a problem or effect. The diagram has four main categories: people, process, technology, and environment. Each category has subcategories that list specific factors that may contribute to the problem or effect. The diagram shows that incorrect configuration under technology was marked as an initial cause of website crash.

NEW QUESTION 204

A project is running over budget, and due to new legislation in the country, the company needs to release all its contractors on the project or hire them as full-time employees. Which of the following should the PM do next to comply with the new legislation?

- A. Use only full-time employees even if the project is delayed.
- B. Hire all team members to avoid any delay in the project.
- C. Close the contract and pay the contractors cash for the remainder of the project.
- D. Look for an overseas vendor to finalize the project work.

Answer: A

Explanation:

In response to new legislation requiring the release of contractors or their conversion to full-time employees, the project manager should prioritize compliance with the law. This may involve using only full-time employees, even if it results in project delays. The focus should be on legal compliance and the ethical treatment of workers, rather than solely on project timelines.

References = The answer is based on standard project management practices and the typical response to changes in legislation affecting project staffing. For detailed information, please refer to the CompTIA Project+ Study Guide and other official CompTIA resources.

NEW QUESTION 208

A PM is responsible for implementing a new customer relationship management system and has learned that the sales organization is reluctant to utilize the new system. The organization's reluctance could jeopardize the success of the project. Which of the following steps should be taken to understand the adoption issues and gain organizational acceptance of the initiative? (Select TWO).

- A. Train users on the proper use of the system.
- B. Escalate the issue to the CCB
- C. Hold sessions to understand user challenges.
- D. Track system usage and report user activity.
- E. Log the issue in the project risk register.
- F. Create a memorandum of acceptable use.

Answer: CD

Explanation:

The project manager should hold sessions to understand user challenges and track system usage and report user activity. These steps will help the project manager to identify the root causes of the adoption issues and monitor the progress of the system utilization. They will also help to communicate with the sales organization and provide feedback and support¹²

NEW QUESTION 213

A PM is working with stakeholders in the discovery phase and comparing the cost of the project to the cost savings the project will produce when it is complete. The output of this exercise will produce the:

- A. ROI.
- B. SOW.
- C. RFI.
- D. RPR

Answer: A

Explanation:

The output of this exercise where the project manager is comparing the cost of the project to the cost savings the project will produce when it is complete will produce the return on investment (ROI). ROI is a financial metric that measures the profitability or efficiency of an investment by comparing its benefits or returns to its costs. ROI can help to evaluate the value or worth of a project and support decision making and prioritization. ROI is calculated by dividing the net benefits (benefits minus costs) by the total costs and multiplying by 100 to get a percentage.

NEW QUESTION 216

A project manager is overseeing the implementation of a major upgrade to a critical ERP system. The project sponsor is requiring that the upgrade should not exceed more than three hours of downtime for the implementation and validation in production. During cutover, the team runs into a validation issue after 2.5 hours, and the process is only 70% through the validation steps Which of the following actions should the project manager take?

- A. Notify customers the downtime will take longer than expected.
- B. Add new team members to help speed up validation.
- C. Begin executing the rollback plan.
- D. Record the issue and proceed with the implementation.

Answer: C

Explanation:

When a critical ERP system upgrade encounters a validation issue and is at risk of exceeding the allotted downtime, the project manager should begin executing the rollback plan. This action is taken to ensure that the system can be restored to its previous state without exceeding the downtime limit, thus minimizing the impact on the business operations.

NEW QUESTION 219

Two project team members are assigned to set up new work areas and are disagreeing about the placement of hardware and peripherals at the end users' desks. The requirements do not specify where to place the items, just what is needed in each space. Which of the following should the project manager do to resolve the conflict?

- A. Send out a survey to the potential end users to gather information about the best functional setup for work productivity.
- B. Provide clear instructions based on personal preference and aesthetics for setup of the work areas.
- C. Explain to team members that the placement of the items is not too important, as long as everything is connected and working.
- D. Facilitate a meeting between team members to review the pros and cons of the different configurations so as to encourage an amicable solution.

Answer: D

Explanation:

This answer is based on the best practice of conflict resolution in project management, which is to use a collaborative or problem-solving approach that seeks a win- win outcome for all parties involved¹². By facilitating a meeting, the project manager can help the team members communicate effectively, understand each other's perspectives, and find a mutually acceptable solution that meets the project requirements. This way, the project manager can also maintain team morale and cohesion, and avoid imposing a decision that may cause resentment or dissatisfaction among the team members³. References = CompTIA Project+ Certification Study Guide⁴, CompTIA Project+ Certification Exam Objectives⁵, How Do You Handle Conflict in Project Management?¹, 7 Strategies for Conflict Resolution in Project Management², The Conflict Resolution Skills Every Project Manager Needs³

NEW QUESTION 222

Two team members have a minor disagreement on how a task should be performed. The project manager plans to meet with the team members to discuss the matter. Which of the following techniques should the project manager use to emphasize the areas of agreement and downplay the opposing views?

- A. Compromising
- B. Forcing
- C. Smoothing
- D. Collaborating

Answer: C

Explanation:

Smoothing is a conflict resolution technique that involves emphasizing the areas of agreement and minimizing the areas of difference. It is useful when the conflict is minor and the relationship between the parties is more important than the issue. Smoothing can help maintain harmony and avoid further escalation of the conflict¹.

NEW QUESTION 224

A project manager prefers to have immediate contact with team members because it allows for faster response times and more interactive discussions. Which of the following communication methods should the project manager use?

- A. Synchronous
- B. Informal
- C. Asynchronous
- D. Formal

Answer: A

Explanation:

The project manager should use synchronous communication methods if they prefer to have immediate contact with team members. Synchronous communication is a type of communication that occurs in real time and allows for faster response times and more interactive discussions. Examples of synchronous communication methods include phone calls, video conferences, instant messaging, and face-to-face meetings. Synchronous communication can help to build rapport, clarify doubts, and resolve issues quickly among team members.

Synchronous communication should be used when the project manager prefers to have immediate contact with team members. Synchronous communication allows for real-time interaction and feedback, enabling faster response times and more interactive discussions. References: CompTIA Project+ Study Guide Section 3.1.3

NEW QUESTION 225

Which of the following provides a layered approach to logging in to systems that contain an organization's most valuable intellectual property?

- A. Remote access
- B. Password protection
- C. Multifactor authentication
- D. Virtual private network

Answer: C

Explanation:

Multifactor authentication (MFA) is a security method that requires users to provide two or more pieces of evidence to verify their identity before accessing a system. MFA can use different types of factors, such as something the user knows (e.g., password, PIN, security question), something the user has (e.g., token, smart card, mobile device), or something the user is (e.g., fingerprint, face, voice). MFA provides a layered approach to logging in to systems that contain an organization's most valuable intellectual property, as it makes it harder for unauthorized users to gain access by compromising one factor alone. MFA can also prevent phishing, brute force, and credential theft attacks¹². References = CompTIA Project+ PK0-005 Certification Study Guide,

NEW QUESTION 229

A financial manager reports that several employees' allocations from the past month appear to be 200% even though they are only assigned to a particular project. Which of the following could MOST likely be the cause of this issue?

- A. A project manager assigned the wrong resources.
- B. A project manager did not release the resources
- C. A project manager did not remove the system access.
- D. A project manager did not provide the project sign-off.

Answer: B

Explanation:

A project manager did not release the resources. A project manager not releasing the resources could most likely be the cause of this issue where several employees' allocations from the past month appear to be 200% even though they are only assigned to a particular project. Releasing resources is a process of freeing up or reallocating any human or material resources that were used for a project after its completion or closure. Releasing resources can help to update the resource availability and utilization records and avoid any conflicts or errors in resource allocation or reporting.

NEW QUESTION 230

A project team is defining operational training, discussing a go-live date, and describing the operational handoff. Which of the following best describes what the team is developing?

- A. The project closeout report
- B. A handover to operations
- C. Phase-gate review documentation
- D. A transition plan

Answer: D

Explanation:

A transition plan is a document that outlines how the project deliverables will be transferred to the operations team or the end users, and how the project team will disengage from the project. It typically includes details such as operational training, go-live date, support arrangements, roles and responsibilities, and acceptance criteria. A transition plan is different from a project closeout report, which summarizes the project performance, lessons learned, and final status. A handover to operations is a process of transferring the project deliverables to the operations team, but it is not a document. A phase-gate review documentation is a set of documents that are used to evaluate the project progress and readiness to move to the next phase, but it is not related to the operational handoff. References = CompTIA Project+ PK0-005 Certification Study Guide, Chapter 14: Closing the Project, p. 409-410; [CompTIA Project+ Certification Exam Objectives], Domain

4: Project Closure, Objective 4.1: Compare and contrast various project closure activities.

NEW QUESTION 234

A PM wants to add a chart to the monthly status report to show major accomplishments for key events. Which of the following is the best chart to use?

- A. Milestone
- B. Gantt
- C. Burndown
- D. PERT

Answer: A

Explanation:

A milestone chart is the best chart to use to show major accomplishments for key events, because it displays the important deliverables or outcomes of a project along a timeline¹². A milestone chart can provide a high-level overview of the project progress and achievements, without showing the details of each task or activity³⁴. A milestone chart can also help communicate the project status and expectations to the stakeholders, and identify any potential risks or delays that may affect the project completion⁵⁶. References = CompTIA Project+ Certification Study Guide⁷, CompTIA Project+ Certification Exam Objectives⁸, What is a Milestone Chart?¹, How to Create a Milestone Chart in Excel in 3 Steps², Milestone Chart: The Easiest Way to Track Project Milestones³, How to Use Milestones in Project Management⁴

NEW QUESTION 236

During an agile project, a team member checked the project artifacts in order to anticipate when all the work should have been completed. Which of the following charts was the team member most likely consulting?

- A. Pareto chart
- B. Milestone chart
- C. Burndown chart
- D. Gantt chart

Answer: C

Explanation:

A burndown chart is a visual representation of the remaining work versus the time required to complete it¹. It is commonly used by agile teams to track the progress of each iteration or sprint and to forecast the project completion date². A burndown chart shows the ideal work remaining line and the actual work remaining line, which can help the team identify any deviations or impediments and adjust accordingly¹. A burndown chart is different from a Pareto chart, which shows the frequency of different causes of problems; a milestone chart, which shows the key events and deliverables of a project; and a Gantt chart, which shows the dependencies and durations of tasks in a project³. References = CompTIA Project+ Study Guide: Exam PK0-005, 3rd Edition, Chapter 6: Planning Projects Part 2, page 173; Burndown Chart: What Is It & How to Use One for Agile - ProjectManager, Introduction and Components of a Burndown Chart sections; Burndown Chart: What it is, How to Use it, Example [2023] • Asana, Introduction and What is a burndown chart? sections.

NEW QUESTION 240

Which of the following pieces of data are examples of PII?

- A. Medical record and test result values
- B. IP address and email address
- C. Name and year of birth
- D. X-ray and blood type

Answer: B

Explanation:

PII stands for personally identifiable information, which is any data that can be used to identify a specific individual. Examples of PII include name, address, phone number, email address, social security number, passport number, driver's license number, etc. IP address and email address are both PII because they can be used to trace the identity and location of a person. Medical record and test result values, name and year of birth, and x-ray and blood type are not PII by themselves, but they can become PII if they are combined with other data that can link them to a specific individual. References = CompTIA Project+ Study Guide: Exam PK0-005, 3rd Edition, Chapter 10: Project Security, page 331. CompTIA Project+ Certification Exam Objectives, Domain 4: Project Security, Objective 4.1: Given a scenario, apply security best practices to a project, Sub-objective: Identify and classify PII.

NEW QUESTION 244

In a functional organization, a project has been completed successfully. Which of the following actions would the project manager MOST likely perform?

- A. Assemble a new project with existing resources.
- B. Obtain the final report from release management.
- C. Notify the functional manager that resources are released.
- D. Allocate resources in a different project

Answer: C

Explanation:

The project manager should notify the functional manager that resources are released after completing a project successfully in a functional organization. A functional organization is a type of organizational structure where employees are grouped by their functions or specialties, such as finance, marketing, or engineering. In a functional organization, the functional manager has more authority and control over the resources than the project manager. Therefore, the project manager should inform the functional manager when the resources are no longer needed for the project and can be reassigned to other tasks or projects.

NEW QUESTION 245

Which of the following contract types in project procurement has the highest risk for the buyer?

- A. Time and material
- B. Cost-plus
- C. Fixed-price

D. Unit price

Answer: B

Explanation:

A cost-plus contract is a type of contract where the buyer agrees to reimburse the seller for the actual costs of the work plus a fee, which can be fixed, percentage, incentive, or award based. This type of contract has the highest risk for the buyer because the buyer has no control over the cost or quantity of the work and the seller has little incentive to control the costs or complete the work efficiently. The seller may inflate the costs or prolong the work to increase the fee. The buyer may end up paying much more than the estimated budget or the market value of the work. References = CompTIA Project+ PK0-005 Certification Study Guide, Chapter 9: Project Procurement Management; CompTIA Project+ Certification Exam Objectives, Domain 3: Project Execution, Objective 3.3: Execute procurement activities.

NEW QUESTION 250

A project team is working remotely from different locations across the country. As part of a lessons-learned exercise, the project manager would like to identify the level of engagement among project team members. Which of the following would be the best tool for the project manager to use?

- A. Meeting chat
- B. Email
- C. Real-time survey
- D. Whiteboard

Answer: C

Explanation:

A real-time survey is a tool that allows the project manager to collect feedback from the project team members in an interactive and timely manner. A real-time survey can measure the level of engagement, satisfaction, motivation, and performance of the team members, as well as identify any issues, challenges, or opportunities for improvement. A real-time survey can also increase the participation and collaboration of the team members, as they can see the results and comments of their peers instantly. A real-time survey is more effective than a meeting chat, an email, or a whiteboard, as it can reach a larger and more diverse audience, provide more structured and quantitative data, and avoid distractions and interruptions. References = CompTIA Project+ Study Guide: Exam PK0-005, 3rd Edition, Chapter 10: Project Closure, p. 367; The 9 best online survey apps in 2023 | Zapier

NEW QUESTION 254

The quarterly financial report displays losses from a project even though the project was completed successfully several weeks ago. Which of the following actions should the project manager perform next?

- A. Remove access.
- B. Complete the project sign-off.
- C. Release the resources.
- D. Outline the lessons learned.

Answer: B

Explanation:

The project sign-off is the formal acceptance of the project deliverables by the client, stakeholder, or customer. It also marks the closure of the project and the release of the final payment. If the project sign-off is not completed, the project may still incur costs and liabilities, which can explain the losses in the financial report. Therefore, the project manager should complete the project sign-off as soon as possible to avoid further losses¹².

NEW QUESTION 255

During the planning phase, a PM reviews the SOW from the contractor, grades the full-time equivalents' resumes, evaluates the titles and salaries, and estimates the number of hours for each milestone by full-time equivalents. The PM is most likely:

- A. negotiating resources.
- B. assigning resources.
- C. assessing the resource pool.
- D. adding resources to the schedule.

Answer: C

Explanation:

Assessing the resource pool is the process of identifying and evaluating the availability, skills, and costs of the resources needed for the project. The PM reviews the SOW from the contractor to understand the scope and requirements of the project, grades the full-time equivalents' resumes to determine their qualifications and suitability for the project, evaluates the titles and salaries to estimate the budget and allocation of the resources, and estimates the number of hours for each milestone by full-time equivalents to plan the schedule and workload of the project¹².

NEW QUESTION 259

Which of the following BEST identifies the intent and purpose of a project closeout report?

- A. To provide documentation of lessons learned
- B. To document variances from the initial project baseline
- C. To validate that a project has been successfully completed
- D. To release resources and terminate all access rights

Answer: C

Explanation:

To validate that a project has been successfully completed. The intent and purpose of a project closeout report is to validate that a project has been successfully completed and to summarize the goals, objectives, and outcomes of the project, as well as the lessons learned and the feedback from stakeholders. A project closeout report is a document that is submitted at the end of a project to officially conclude it and release the resources and contracts involved. It is useful for

evaluating the project's success and improving the performance of future projects¹²

NEW QUESTION 263

An organization was fined due to an audit finding that revealed a third-party vendor was able to see secured project information in a recently implemented system. Which of the following was the cause of this situation?

- A. The ticket system provided access by default without any approval.
- B. The project manager did not perform proper project planning.
- C. The system is lacking proper access controls.
- D. Sensitive data was incorrectly classified during the audit process.

Answer: C

Explanation:

The system is lacking proper access controls if a third-party vendor was able to see secured project information in a recently implemented system that resulted in a fine for the organization. Access controls are security mechanisms that regulate who or what can view, use, or modify data or resources in a system or network. Access controls typically involve authentication and authorization processes that verify the identity and permissions of users or devices before granting them access. Access controls can help to protect data confidentiality, integrity, and availability and prevent unauthorized access, misuse, or theft¹²

NEW QUESTION 265

A project manager was not part of a contract negotiation. The project manager is concerned that stakeholders will expect the project to achieve deliverables requested in the RFP Which of the following documents should the project manager produce FIRST to start communication about the boundaries of the project?

- A. Milestone chart
- B. Work breakdown structure
- C. Project charter
- D. Detailed scope statement

Answer: C

Explanation:

The project manager should produce a project charter first to start communication about the boundaries of the project. A project charter is a document that formally authorizes a project and defines its high-level scope, objectives, assumptions, constraints, stakeholders, roles and responsibilities, and key deliverables. A project charter can help to communicate the project vision and expectations to all stakeholders and provide a basis for future project decisions²³

NEW QUESTION 266

A new junior PM who has ownership of a project does not understand how to manage conflicts involving multiple personalities. Which of the following is the best order of the stages the PM should follow to nurture the team to high performance?

- A. Forming, storming, performing, norming, adjourning
- B. Forming, performing, storming, norming, adjourning
- C. Forming, norming, storming, performing, adjourning
- D. Forming, storming, norming, performing, adjourning

Answer: D

Explanation:

This is the correct order of the stages of team development according to Tuckman's model¹²³. The forming stage is where team members first meet and get acquainted. The storming stage is where team members experience conflicts and disagreements. The norming stage is where team members resolve their differences and establish norms and rules. The performing stage is where team members work together effectively and efficiently. The adjourning stage is where team members complete the project and celebrate their achievements. References = CompTIA Project+ Study Guide: Exam PK0-005, 3rd Edition, Chapter 6: Project Team Management, p. 197; The 5 Stages of Team Development (Including Examples) | Upwork; The 5 Stages of Team Development - Teamwork; Using the Stages of Team Development | MIT Human Resources

NEW QUESTION 267

Which of the following would be MOST beneficial to do before a call to ensure all meeting items are addressed and the correct participants attend?

- A. Assign action items to attendees.
- B. Distribute an agenda.
- C. Email the minutes from the previous meeting.
- D. Schedule a convenient time.

Answer: B

Explanation:

The project manager should distribute an agenda before a call to ensure all meeting items are addressed and the correct participants attend. An agenda is a document that outlines the purpose, topics, and objectives of a meeting. It also includes information such as date, time, duration, location, attendees, and roles. Distributing an agenda can help to prepare the participants for the meeting, set clear expectations, and facilitate a productive and focused discussion¹²

NEW QUESTION 272

A critical business initiative introduced new processes and technology to the organization. Which of the following approaches should be used to ensure the deliverables are increasingly adopted and leveraged by the organization over time?

- A. Creation of a social news forum
- B. Management directives to use the new system
- C. New user kickoff meeting
- D. Monthly feedback and training sessions

Answer: D

Explanation:

Monthly feedback and training sessions are the best approach to ensure that the deliverables of a critical business initiative are increasingly adopted and leveraged by the organization over time. Feedback and training sessions are communication and learning activities that provide information and guidance on how to use and benefit from the new processes and technology introduced by the initiative. Feedback and training sessions can help to increase awareness, understanding, acceptance, and adoption of the deliverables among the organization's employees and stakeholders. They can also help to identify and address any issues or challenges that may arise during the implementation and transition phases.

NEW QUESTION 276

In the initiation phase, a PM is reviewing the objectives, the high-level requirements, the success criteria, and the budget resources. Which of the following action items will benefit from this analysis?

- A. Developing a RACI
- B. Identifying and assessing stakeholders
- C. Assigning project resources
- D. Establishing communication channels

Answer: B

Explanation:

Identifying and assessing stakeholders is an action item that will benefit from the analysis of the objectives, the high-level requirements, the success criteria, and the budget resources in the initiation phase. By reviewing these elements, the PM can determine who are the key individuals or groups that have an interest or influence in the project, what are their expectations and needs, and how to engage them effectively throughout the project life cycle12.

NEW QUESTION 277

Which of the following would be the NEXT document a project manager should update once the need to procure goods and/or services is identified?

- A. Memorandum of understanding
- B. Request for information
- C. Statement of work
- D. Non-disclosure agreement

Answer: B

Explanation:

The statement of work (SOW) would be the next document that a project manager should update once the need to procure goods and/or services is identified. A SOW is a document that defines the scope, deliverables, schedule, and terms and conditions of a project or contract. A SOW typically includes information such as purpose, scope of work, location of work, period of performance, deliverables schedule, applicable standards, acceptance criteria, special requirements, and payment schedule. A SOW can help to establish a common understanding and agreement between the client and the service provider on what needs to be done and how it will be done.

NEW QUESTION 278

Which of the following should be considered first when determining the privacy management for project data?

- A. Evaluating the current privacy protection program
- B. Understanding applicable privacy regulations
- C. Maintaining awareness of industry best practices
- D. Implementing security role-based controls

Answer: B

Explanation:

Before starting a new project that involves personal data, the project manager should first understand the relevant privacy regulations that apply to the data subjects, the data controllers, and the data processors. These regulations may vary depending on the location, industry, and nature of the data. For example, GDPR applies to any project that processes the personal data of individuals in the European Union, regardless of where the project is based or executed. Understanding the applicable privacy regulations will help the project manager to identify the legal obligations, risks, and compliance requirements for the project data. References = CompTIA Project+ Study Guide, Chapter 3: Project Planning, Section 3.4: Data Privacy and Security, p. 121-122; A Project Management Approach to Data Protection Compliance; 10 Data Protection Considerations Before Starting a New Project; Project Teams Must Manage Risk and New Requirements to Ensure Data Privacy

NEW QUESTION 283

A project manager is leading the implementation of a new service for a well-known, global company for which brand image is most important. The project will rely on contracted services. As part of the request for proposal process, the project team has identified a short list of vendors to submit proposals. Which of the following items should the project team consider as a primary factor to remove a vendor from consideration?

- A. The vendor's proposed schedule does not align with the desired schedule.
- B. The vendor is new and not well established in the market.
- C. The vendor has been linked to ESG concerns within the past month
- D. The vendor's quote was the highest of all the proposals.


Answer: C

Explanation:

ESG stands for environmental, social, and governance, and it refers to the criteria that measure the sustainability and ethical impact of an organization. ESG concerns can affect the reputation, performance, and value of a company, as well as its stakeholders and customers. For a well-known, global company that values its brand image, hiring a vendor that has been linked to ESG concerns can be a major risk and a source of negative publicity. Therefore, the project team should consider this as a primary factor to remove a vendor from consideration12.

NEW QUESTION 285

A project team member wrote a user guide over the past ten days. Given the following scatter diagram.

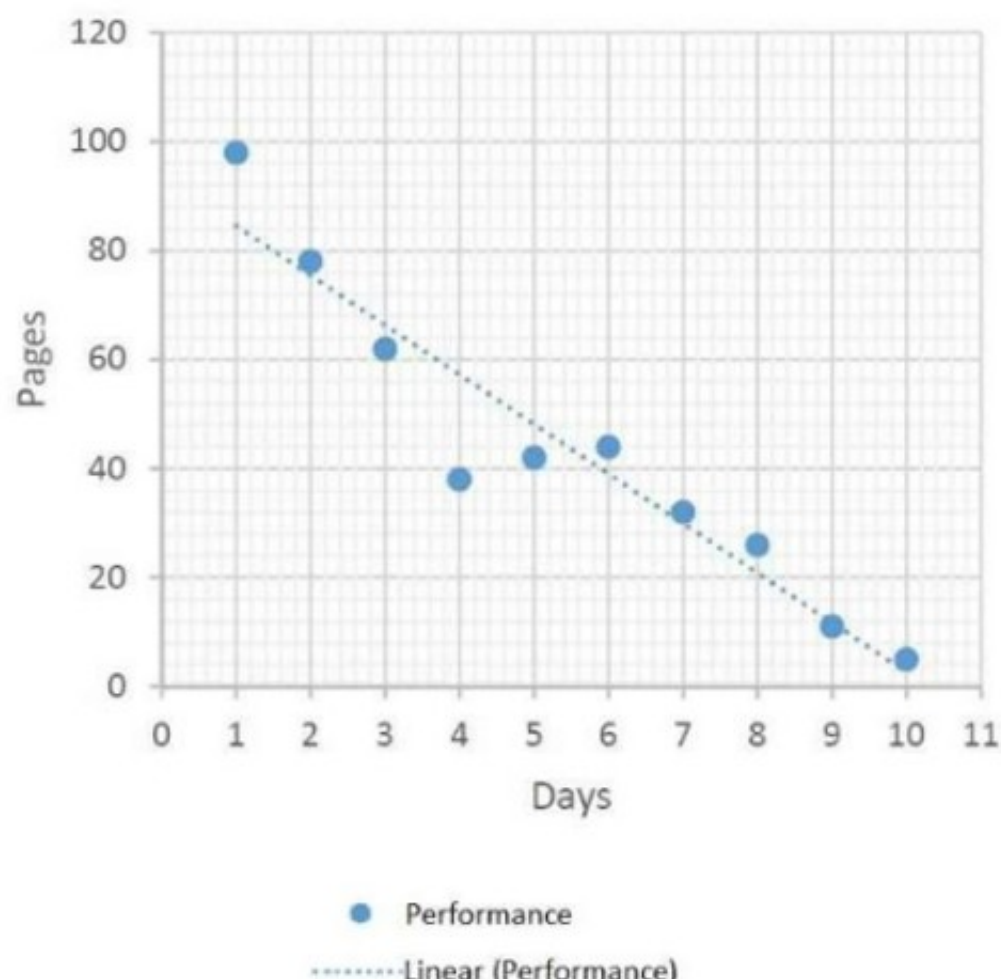

Which of the following can be formally conducted?

- A. The team member prioritized other tasks over the completion of this task
- B. The team member had performance issues over time.
- C. There is a negative correlation between time and output
- D. This is a display of units of outstanding work to predict completion

Answer: C

Explanation:

The scatter diagram shows a clear negative correlation between time (days) and output (pages), meaning as time progresses, the number of pages completed decreases. This is evident from the downward trend of the plotted points on the graph. References = CompTIA Project+ Certification Study Guide, Chapter 3: Project Execution, page 130; CompTIA Project+ Certification Exam Objectives, Domain 3.0: Project Execution, Objective 3.3: Analyze project performance by using appropriate tools and techniques, Sub-objective 3.3.2: Given a scenario, interpret the results of data analysis using appropriate tools and techniques, Knowledge of: Scatter diagrams.

NEW QUESTION 290

.....

THANKS FOR TRYING THE DEMO OF OUR PRODUCT

Visit Our Site to Purchase the Full Set of Actual PK0-005 Exam Questions With Answers.

We Also Provide Practice Exam Software That Simulates Real Exam Environment And Has Many Self-Assessment Features. Order the PK0-005 Product From:

<https://www.2passeasy.com/dumps/PK0-005/>

Money Back Guarantee

PK0-005 Practice Exam Features:

- * PK0-005 Questions and Answers Updated Frequently
- * PK0-005 Practice Questions Verified by Expert Senior Certified Staff
- * PK0-005 Most Realistic Questions that Guarantee you a Pass on Your FirstTry
- * PK0-005 Practice Test Questions in Multiple Choice Formats and Updatesfor 1 Year
